West Contra Co
ied School District

March 14, 2012

TOTAL SCHOOL SOLUTIONS
4751 MANGELS BOULEVARD
FAIRFIELD, CA 94534

Revised: March 14, 2012

TABLE OF CONTENTS

INTRODUCTION **1**

EXECUTIVE SUMMARY **2**

,1'(3(1'(17 3(5)250$1&($8',725¶6 5(3257 ..... **3**

COMPOSITE BOND MEASURES FINANCIAL REPORT **4**

Oon1 02.02RABT M 07 m [(8.07NABT 2.021 376M-10<0033N.....22(..1-459.79T 0 0 1 0 0 1 309.05 680.5 Tm 30 ...459.79T 0 0 .....)] TJ ET BT 1 0 0 1 546.1 625.3 Tm [( )] TJ 327 ...459.79T 0 0 .....)] TJ ET BT 1 0 0 1 546.1 625.3 Tm [( )] TJ 423....459.79T 0 0 .....

EXECUTIVE SUMMARY

This performance audit, conducted by Total School Solutions (TSS), is the annual audit of the $300 million Measure D (2002), $400 million Measure J

2008-09

7KH ³7UDQVIHUV 1HW´ ILJXUH RI Building Fund (Fund 21) to the County School Facilities Fund (Fund 35 WR SURYLGH WKH 'LVWULFW¶V PDWFK for approved modernization projects. The $121,500,000 source of funds in 2008-09 was the sale of Measure J bonds.

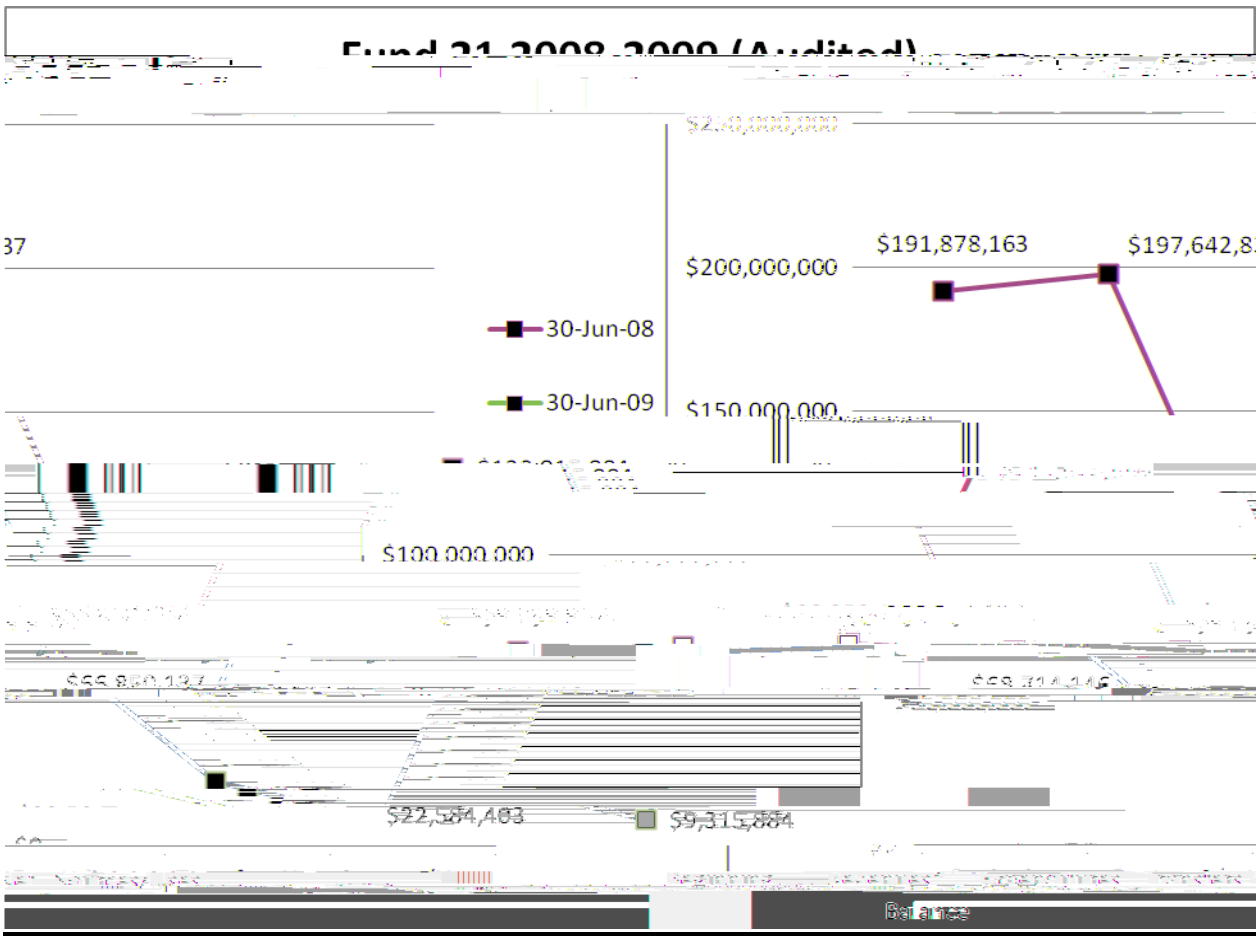

2009-10

Proposition 39 Bond Sale Limitations

Proposition 39, passed by California voters on November 7, 2000; Assembly Bill 1908, which became law on June 27, 2000; and Assembly Bill 2659, which became law on September 22, 2000, established limitations on bonds that may be issued. The first limitation is the bonding capacity of the District, which is based on 2.5 percent of assessed valuation (A/V), which may be increased through a waiver request to the State Board of Education. The second limitation is a maximum tax rate of $60.00 per $100,000 of A/V for each bond measure, which may not be increased by filing a waiver request. These two provisions are more fully described in Education Code Section 15106:

> Any unified school district or community college district may issue bonds that, in aggregation with bonds issued pursuant to Section 15270, may not exceed 2.5 percent of the taxable property of the district as shown by the last equalized assessment of the county or counties in which the district is located.

However, as noted above, the 2.5 percent limitation may be waived by the California Board of Education if a school district demonstrates sufficient justification for a waiver.

7KH 'LVWULFW¶V UHFHQW DVVHVVHG YDOXDWLRQ DQG ERQG

Fiscal Year	Total A/V	Annual % Change	Bonding Capacity@ 2.5%	Bonding Capacity @ 5.0%

Resolution No. 25- RUGHULQJ WKH 0HDVXUH - ERQG HOHFWLRQ V
be issued unless the District shall have received a waiver from the California State Board of
Education of the District ¶V VWDWXWRU\ GHEW OLPLW LQ 2008, At its meeting on January 21, 2010, the
Board authorized the administration to submit a waiver request to the SBE to increase the
'LVWULFW¶V 0HDVXUH - ERQGLQJ OLPLW WR SHUFHQW R
WKURXJK 0D\ 7KH 6%(DSSURYHG WKH 'LVWULFW¶V ZDL
2009, which enabled the District to issue $105 million of its remaining authorization of $210
million Measure J bonds. During the 2009-10 fiscal year, the District issued $132.5 million of
Measure J bonds, bringing the remaining authorization to $77.5 million. Because Measure J was
at its $60 lim

Commendations

- The District is commended for refunding prior bond issuances to keep its tax rate below $60 per $100,000 of assessed valuation.

- The District is commended for obtaining increases in its bonding capacity to enable bonds to be sold.

Conclusion

- By restructuring debt and increasing bonding capacity, the District has been able to continue with its Bond Program without delay in spite of declining assessed valuation.

The complete ballot language contained in Measure D (2002) is included in Appendix B. The following appeared as the summary ballot language:

> To complete repairing all of our schools, improve classroom safety and relieve overcrowding through such projects as: building additional classrooms; making seismic upgrades; repairing and renovating bathrooms, electrical, plumbing, heating and ventilation systems, leaking roofs, and fire safety systems; shall the West Contra

$V UHTXLUHG E\ 3URSRVLWLRQ WKH 'LVWULFW HVW
Committee. On April 19, 2003, the Board of Education merged the Measure M and Measure D oversight committees into one body, with the caveat that the new committee would use the more stringent requirements for oversight set forth in Proposition 39.

Based on the Capital Assets Management Plan dated July 25, 2011, the District had expended $259.7 million (86.6 percent) of the Measure D authorization. All expenditures of Measure D funds during this reporting period were for projects within the scope of the ballot language. TSS finds the West Contra Costa Unified School District in compliance with the language contained in Resolution 42-0102.

Measure J (2005)-- On July 13, 2005, the Board of Education of the West Contra Costa Unified School District approved the placement of a $400 million bond measure (Measure J) on the ballot with the adoption of Resolution No. 25-0506. Measure J, a Proposition 39 bond

The complete ballot language contained in Measure D is included as Appendix D. The following appeared as the summary ballot language:

> To make schools safe, complete essential health/safety repairs, qualify for State matching grants, shall West Contra Costa Unified School District upgrade schools for earthquake safety/handicap accessibility, remove asbestos, upgrade restrooms, vocational classrooms/technology/energy systems to reduce costs, install lighting and security systems, acquire repair, construct, equipment/sites/facilities, by issuing $380,000,000 in bonds within legal rates and bonding capacity limits with L Q G H S H Q G H Q W D X G L W V F L W L] H Q R Y H U V L J K W D Q G Q

The Measure D (2010) ballot language focused on the continued repair, modernization, and reconstruction of District school facilities in the following broad categories:

PRIORITY SCHOOL PROJECTS LIST

- School Renovation, Repair and Upgrade Projects
- School Health, Safety and Security, Earthquake Safety and Energy Efficiency School Projects
- District-Wide Wiring and Instructional Technology For Effective Learning Environment and Job Training Projects
- New Construction Education Enhancement/Class Size Reduction Projects at School Sites

As required by Proposition 39, the West Contra Costa Unified School District certified the results of the June 8, 2010, bond (Measure D) election at the school board meeting of tiresuuer/14(t BT1

As of June 30, 2011, the District has issued the following bonds:

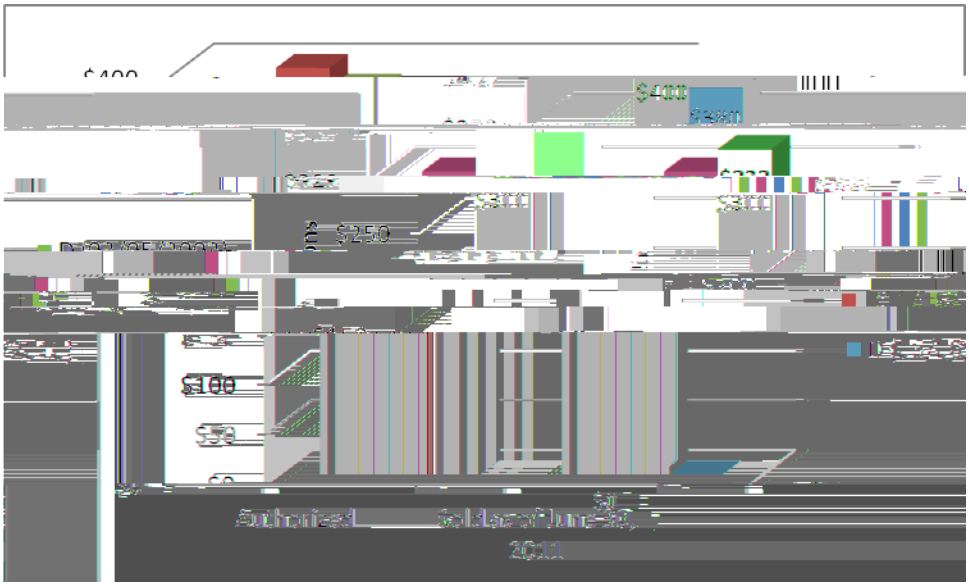

Authorized Total: $1,080 billion
Sold as of June 30, 2011: $622.5 million

Total Measure D (2002), J (2005) and D (2010) expenditures totaling $437,689,334 as of June 30, 2011, are 40.5 percent of the $1,080 billion authorization. All of the expenditures of bond funds were for projects within the scope of the ballot language.

Proposition 39 Bond Sale Limitations

Proposition 39, passed by California voters on November 7, 2000; Assembly Bill 1908, which became law on June 27, 2000; and Assembly Bill 2659, which became law on September 22, 2000, established limitations on bonds that may be issued. The first limitation is the bonding capacity of the District, which is based on 2.5 percent of assessed valuation (A/V), which may be increased through a waiver request to the State Board of Education. The second limitation is a maximum tax rate of $60.00 per $100,000 of A/V for each bond measure, which may not be increased by filing a waiver request. These two provisions are more fully described in Education Code Section 15106:

> Any unified school district or community college district may issue bonds that, in aggregation with bonds issued pursuant to Section 15270, may not exceed 2.5 percent of the taxable property of the district as shown by the last equalized assessment of the county or counties in which the district is located.

However, as noted above, the 2.5 percent limitation may be waived by the California Board of Education if a school district demonstrates sufficient justification for a waiver.

7KH 'LVWULFW¶V UHFHQW DVVHVVHG YDOXDWLRQ DQG ER

Fiscal Year	Total A/V	Annual % Change	Bonding Capacity 2.5%	Bonding Capacity 5.0%
2011-12	$22,170,563,072	1.1	$554.3 million	$1,108.5 billion

Source: District Board Item F.1, September 21, 2011, Preliminary Official Statement for the sale of $100 million, Measure D (2010) bonds consisting of $21 million QSCB bonds and $79 million general obligation bonds, citing California Municipal Statistics, Inc.

Education Code Section 15270 further adds:

> The tax rate levied to meet the requirements of Section 18 of Article XVI of the California Constitution in the case of indebtedness incurred pursuant to this chapter at a single election, by a unified school district, shall not exceed sixty dollars ($60) per one hundred thousand dollars ($100,000) of taxable property.

On July 10, 2002, the Board of Education of the West Contra Costa Unified School District authorized the administration to submit a waiver request to the California State Board of Education (SBE) to increase the District ¶V ERQGLQJ OLPLW IURP 0 percent of SHUFH assessed valuation (A/V). At the SBE meeting of November 13-14, 2002, the SBE approved the waiver request for Measures E, M, and D only.

Resolution No. 25-

Commendation

- The District, being unable to sell additional Measure J bonds, is commended for its actions to seek a $380,000,000 Measure D (2010) bond measure to enable the bond program to continue without delay.

Conclusions

- Measures D (2002), J (2005) and D (2010) had a combined balance of $110.1 million as of June 30, 2011, thereby enabling the District to continue implementing its bond program.

- TSS finds the West Contra Costa Unified School District in compliance with the Measures D (2002), J (2005) and D (2010) ballot languages.

Recommendation

-

COMPLIANCE WITH STATE LAW AND REGULATIONS

Objective

The objective of this section is to assess the overall compliance with some of the pertinent legal and regulatory requirements governing a school district facilities program. TSS has developed this assessment of compliance to analyze the functionality of the District ¶ V E R Q G facilities program. It should not be viewed or relied upon as a legal opinion or a complete analysis of all state law and regulationsETBT1 0 0 1 191.9 61W.98 Tm g1.9 61W.98 Tm g1.9 61lW.98 <</M

58 - Rehabilitation
61 - Emergency Repair Program

As of June 30, 2011, the District received state grant amounts summarized in the table below, which includes $12,841,930 received in 2003 (matching District funds from Measure E) for Lovonya DeJean Middle School to $20,387,452 received in 2011 for Overcrowding Relief and Modernization. All of the following financial data was extracted from the OPSC internet website, which maintains a record of the current project status for all school districts in California.

State Facilities Funding

[1] Lovonya DeJean Middle School was approved for state funding on December 18, 2002, with a 50/50 PDWFK 7KH PDMRU IXQGLQJ IRU WKH SURMHFW FDPH IURP WKH 'LVW
[2] These nine projects were Quick-Start projects funded with 60 percent State Funding (60/40) and 40 percent Measure M bonds.
[3] These nine projects were Measure M-1A projects funded with 60/40 matches and Measure M bonds.
[4] These eight projects were Measure M-1B projects funded with 60/40 matches and Measure M bonds.
[5] The Downer Elementary School modernization project is a 60/40 match with Measure D bonds.
[6] The Helms Middle School modernization project is a 60/40 match with Measure D bonds.
[7]

In addition to the above state funds received, the District expects to receive additional state funds for emergency repair projects, overcrowded relief projects, seismic mitigation, additional modernization projects and new construction projects.

The District is in compliance with SAB regulations for all applications it has filed to receive state funding.

State Law Regarding Construction Bidding and Contracting

Many requirements for the construction of public schools appear in different California codes accompanied by regulations from various agencies. The West Contra Costa Unified School District complies with these requirements through its contract documents. The District also provides Notice to Bidders by referencing and detailing the section requirements, as appropriate.

By state law, a number of items are required to appear in bid documents. To verify that these items were included in the District's bid documents, a random selection was made and analyzed, as follows:

Kennedy High School Concession Stand and Lights ±Bid #J068266

Architect: Powell & Partners, DSA #110673, Stamp Date: February 22, 2010
Board Approval of Low Bid of $990,000 by B-Side, Inc.:
January 19, 2011 and February 2, 2011

All sections listed below except Section 00805.6, Labor Compliance Program, were included in the bid documents. Certification of LCP is not required if state match funds are not involved. (See separate section for a discussion of LCP requirements.)

El Cerrito High School Multi-Purpose Sports Field ±Bid #J068267

Architect: WLC Architects, Inc., DSA #111173, Stamp Date: August 3, 2010
Board Approval of Low Bid of $3,749,000 by Michael Paul Corp,
January 19, 2011

All sections listed below except Section 00805.6, Labor Compliance Program, were included in the bid documents. Certification of LCP is not required if state match funds are not involved. (See separate section for a discussion of LCP requirements.)

Ohlone Elementary School Phase I ±West Campus ±Bid #J068272

Architect: Powell & Partners, DSA #111365, Stamp Date: March 22, 2011
Board Approval of Low Bid of $16,961,000 by Zovich Construction:
June 28, 2011

All sections listed below, including Section 00805.6, Labor Compliance Program, were included in the bid documents.

All three of the bid documents reviewed identified above included Section 00700, General Conditions, Articles I-XXVII. The District periodically reviews and revises the General &RQGLWLRQV VHFWLRQ LQFOXGHG LQ WKH 'LVWULFW¶V approved by legal counsel. According to SGI program managers, the most recent review and approvals by legal counsel were in April and July 2010.

Required state items to be included in the bid documents, and District section numbers, included the following:

Section	Description
N/A	Certification Page: Division of the State Architect (DSA) approval for individual project/plans and specifications.
00100	Notice To Bidders: The Notice To Bidders includes the required notification for SURMHFW LGHQWLW\ GDWH WLPH DQG SOH requirements for the type of construction and the validity of that license; bid bond and certified bid security check requirements; payment bond requirements; performance bond requirements; substitution of securities information; definition of prevailing wage requirements; statement establishing blind bid process; and a reservation of the right to reject all bids.
00150	Bid Bond: A bid bond is present in the package and demanded of the contractor on a form prepared by the District, as required.
00330	Non-collusion Affidavit: A non-collusion affidavit form is provided and demanded of the contractor.
00550	Escrow Agreement for Security Deposits in Lieu of Retention: This item is included as an option, as required.
00610	Performance Bond: A performance bond for 100 percent of the contract price, on a form prepared by the District, is demanded of the contractor and included in the bid package.
00620	Payment Bond: A payment bond for 100 percent of the contract price, on a form prepared by the District, is demanded of the contractor and included in the bid package.
00905	:RUNHUV¶ &RPSHQVDWLRQ The contractor is required to certify compliance with VWDWH ZRUNHUV¶ FRPSHQVDWLRQ UHJXODWLRQV
00910	Prevailing Wage and Related Labor Requirements Certification: The contractor is required to certify compliance with the State Public Works Contract requirements.
00911	Apprenticeship Resolution Compliance: The contractor is required to meet the requirements of Labor Code 1777.5.

00912 Disabled Veteran Business Enterprise (DVBE) Participation Certification The contractor is required to certify compliance with the DVBE requirements as set

On February 20, 2009, SBX2 9 was signed into law. It reestablished the LCP for school district facility construction projects that receive State bond funds. The previous LCP program required school districts to provide LCP services directly or through third-party providers. SBX2 9 requires the Department of Industrial Relations (DIR) to directly enforce prevailing wage requirements. Funding for this process would be provided by a fee from the School Facilities Program equal to 0.25 percent of the State funding. This fee would be provided directly to the DIR for enforcement of labor compliance. School districts that have an approved in-house LCP at the time the new regulations are established may apply for an exemption from the new fee. If a school district contracts with a third-party LCP provider, such services may not be eligible for this exemption.

Regardless of whether a school district is required to have a LCP for State-funded projects, it must fully comply with the prevailing wage law. To ensure compliance with the law, a school district should develop and implement policies and procedures to be applied to all construction projects, regardless of the source of funding and the party that bears responsibility for LCP enforcement.

The District currently contracts with a third-party provider for labor compliance services to review contractoBT9(c)284or ide 0 0 1 90.024 478.75 Tm[(og)1ds om thecompliance

Observations

- $ UHYLHZ RI WKH &%2&¶V PDWHULDOV ZHEVLWH SRV CBOC is mostly compliant with the law and BP/ARs although, in some cases, information had not been updated on a timely basis, information on some scheduled meetings was unavailable and annual reports for 2009 and 2010 are posted, but difficult to retrieve.

- The General Conditions included in the bid documents did not identify a version number or date of legal review and approval. A periodic review and subsequent notation ensures the District is keeping abreast of any changes required in the General Conditions.

Commendations

- The District is commended for utilizing all available state funding programs to maximize revenues to meet its IDFLOLWLHV¶ needs.

- The District is commended for developing hazardous materials requirements to meet local conditions for inclusion in bid documents and with which contractors must comply.

- The District is commended for developing a Local Capacity Building Program to encourage participation by local and small business owners and District residents in awarding and managing its public contracts, including District requirements regarding apprenticeship workers.

Conclusion

- The District is in compliance with those state laws and regulations analyzed in this section, with the exception of observations made as documented above. The recommendations made below are intended to enable the District to more effectively carry out its bond program.

Recommendation

- It is recommended that the General Conditions included in the bid documents include a version number and date of legal review and approval. If select sections have been revised, those revisions should be noted.

During the years following Board action regarding Option 1C, a number of variables have influenced construction costs. Those variables include, but are not limited to, the following items that are beyond the control of the District.

- Passage of Proposition 39 (November 2000) and the 55 percent threshold for local bonds and resulting construction;
- Passage of Proposition 1A (November 1998), $9.2 billion bonds and resulting construction;
- Passage of Proposition 47 (November 2002), $13.05 billion bonds and resulting construction;
- Passage of Proposition 55 (March 2004), $10.0 billion bonds and resulting construction;
- Passage of Proposition 1D (November 2006), $10.4 billion bonds and resulting construction;
- Acceleration of construction costs at a rate higher than projected (e.g., Katrina impact);
- Reduction in construction costs due to the recession (aka, a favorable bidding climate);
- Labor compliance law requirements; and
- Inadequate School Facilities Program funding.
- Increased consumption of construction materials by emerging economies.

The cumulative impact of external and internal factors on project budgets made adherence to the Option 1C cost per foot standard impossible to achieve. Furthermore, the District established a goal to deliver high quality projects to the community for the benefit of all students in the District. To meet this goal, it became necessary for the Board to make decisions that resulted in

Project Labor Agreement (PLA)

The Board of Education initially approved a Project Labor Agreement on April 9, 2003. The PLA of April 9, 2003, includes the following stated purpose:

> The purposes of this Agreement are to promote efficient construction operations on the Project, to ensure an adequate supply of skilled craftspeople and to provide for peaceful, efficient and binding procedure for settling labor disputes. In so doing, the parties to this Agreement establish the foundation to promote the public interest, to provide a safe work place, to assure high quality construction, to ensure an uninterrupted construction project, and to secure optimum productivity, on-schedule performance and District satisfaction.
>
> It is the intent of the Agrt s-3(s)239.09 733.44 Tm[( )] 6.81nt of the mct,

DISTRICT AND PROFESSIONAL SERVICES STAFFING PLAN FOR THE BOND PROGRAM

Objective

To gain an understanding of th H ' L V W U L F W ¶ V S R O L F L H V D Q G S U R D F H consultant staffing for managing the measures D (2002), J and D (2010) projects and the effectiveness of the staffing related to the number of bond program projects.

DISTRICT STAFFING FOR THE FACILITIES BOND PROGRAM
(Source: District records)

District Staff Position	Other Funds Percent	Bond Fund Percent	Object Code
Bond Finance Office			
Executive Director of Business Services	25	75	2310
Principal Accountant	0	100	2410
Senior Budget Control Clerk	0	100	2410
Senior Account Clerk	50	50	2410
Bond Finance Office Subtotal	**0.75 FTE[1]**	**3.25 FTE[1]**	
Bond Management Office			
Associate Superintendent of Operations	50	50	2130
District Engineering Officer	10	90	2310
School Facilities Planning Specialist	0	100	2410
Director of Facilities and Construction	10	90	2310
Bond Regional Facility Project Manager	10	90	2310
Bond Regional Facility Project Manager	10	90	2310
Network Planner[2]	10	90	2310
Bond Management Office Subtotal	**1.00 FTE[1]**	**6.00 FTE**	

BOND PROGRAM STAFFING

Category	FTE[1]

provide the District with a more accurate and timely picture of the bond program budgets and schedules.

- Since there have been discussions about the cost of the Scheduler and the Master

PROGRAM MANAGEMENT

Objective

7R JDLQ DQ XQGHUVWDQGLQJ RI WKH 'LVWULFW¶V SURFHVV (2010) programs and the effectiveness of the use of staff and consultants in the management and implementation of the planning, design and construction of the program projects.

Scope and Methodology

In the process of developing this section TSS staff interviewed District staff and consultants to review the process of managing the bond programs and the projects within each program. The IROORZLQJ GRFXPHQWV ZHUH REWDLQHG WKURXJK WKH 'LV this section:

- Capital Assets Management Plan, No. 58, July 25, 2011.

Background

,Q WKH SDVW WKH 'LVWULFW¶V VWUXFWXUH LQYROYHG WKH XVH RI PDQDJL program and project management and placed these tasks within the scope of the primary Construction Manager for the District. The District also employed the use of a Master Architect to define the scope and standards for projects. The District additionally employed the services of a Design Manager to oversee the process of the design teams hired for individual projects. In a review of the scope of services for these consultants in the 2009-

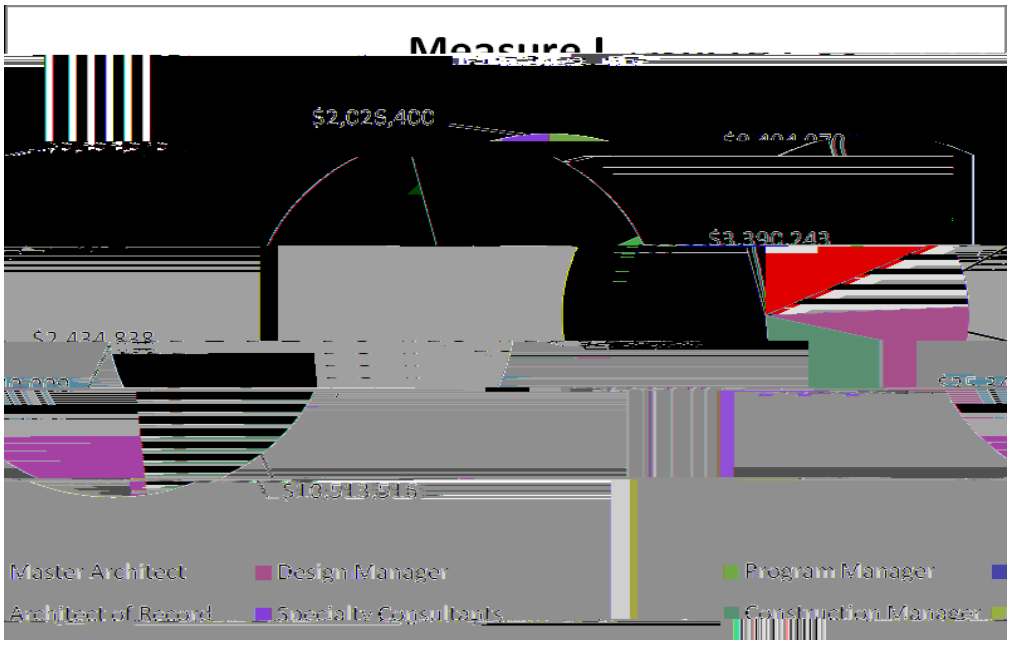

Subtotal Measure J: $53,199,985

Subtotal Measure D (2010): $8,529,451

DESIGN AND CONSTRUCTION COSTS AND BUDGETS

Objective

The objective of this section is to gain an understanding of the established District process for the development and adherence to design and construction budgets on bond funded projects in the facilities construction program; to gather and test data in order to determine compliance and measure the effectiveness of controls.

7 K H I R O O R Z L Q J W D E O H 3 & R Q V W U X F W L R Q V Z R U N H [D P S O H V $
projects bid and awarded during the period from July 1, 2010 through June 30, 2011. During this period, bidder participation ranged from 2 to 13 bidders and was significantly higher compared to the previous years.

SEISMIC MITIGATION

School Site	Seismic Mitigation Status
Adams Middle School	Closed after Seismic Evaluation
Crespi Middle School (Gym and Cafeteria)	Pending evaluation. Application submitted to the DSA for review.
Downer Elementary School	Demolished and replaced.
El Cerrito High School	Demolished and replaced.
Kennedy High School (Granada)	Pending evaluation.
Pinole Valley High School	Demolition and replacement under way.
Richmond High School (Old Gym and Lockers)	Demolition and replacement under way.
Gompers High School (Roosevelt Junior High)	Demolition and replacement under way.
Del Mar School	Sold.
Mira Vista Elementary School (K-8)	Seismic renovations.
King Elementary School (Pullman)	Demolition and replacement under way.
Vista Hills High School	

BIDDING AND PROCUREMENT PROCEDURES

Objective

To gather data and verify that District bidding and awarding of bond funded construction projects comply with the requirements of the Public Contracting Code, state and other relevant laws and regulations.

Scope and Methodology

The scope of this section covers the activities of the District relating to the bidding and awarding of construction contracts for projects funded under the Measure D and J bond program for the period from July 1, 2010 through June 30, 2011. TSS conducted interviews with the District staff, program management staff, members of the Board of Education and the members of the &LWL]HQV¶ %RQG 2YHUVLJKW &RPPLWWHH &%2& ,Q WKH reviewed Board agenda items, bid documents and contract documents for the following:

- Verification that bids were advertised in accordance with public contract code;
- Verification of bid results and board approval;
- Verification that contract documents, notices of award, notices to proceed, and other pertinent documentation was processed for the construction projects.

Background

Public Contract Code, Section 20111, known as the formal bid process requires competitive ELGGLQJ IRU SXEOLF SURMHFWV VXEMHFW WR WKH OLPLV Office, through official advertisement in a newspaper of general circulation. Section 20111 likewise requires competitive bidding on purchases or lease of equipment, materials or supplies; services, not including construction services, or special services and advice in accounting,

With respect to the bid documents, the District uses three different sets of front-end documents. The District also has a Project Labor Agreement (PLA) with various construction unions. The PLA was designed to promote efficient construction operations, ensure adequate supply of skilled craftspeople, and provide procedures for settling labor disputes. The PLA is applied to bond projects more than $1 million in value.

California Uniform Public Construction Cost Accounting Act (CUPCCAA).

Public Contract Code 22030 – 22045, otherwise known as the California Uniform Public Construction Cost Accounting Act (CUPCCAA), is regarded by the California

After reviewing the bid documents, the District declared Pinguelo Construction as the lowest UHVSRQVLEOH ELGGHU ZLWK D UHVSRQVLYH ELG IRU WKH S shown in the bid tabulation document. Award of contract was approved by the Board of Education on October 6, 2010. The Notice of Award was issued on November 10, 2010. Upon receipt of the required contract documents ² the signed contract agreement, bid securities, and other documentation ² the Notice to Proceed was issued on November 10, 2010 The Notice to Proceed specified that the contract commenced on October 27, 2010, with an anticipated date of completion on January 27, 2011.

Kennedy High School Restroom Building and Field Lighting ±# J068266

The Bid Advertisement for the project was published on December 12, and 19, 2010, in the West

El Cerrito HS Multi-Use Sports Fields - # J068267

The Bid Advertisement for this project was published on December 12, and December 19, 2010, in the West County Times. The notice to bidders was advertised on two separate occasions seven days apart; there were at least 14 days between the first bid publication and bid opening as required by law. The bids were opened on January 12, 2011. A total of eleven bids were received. The table below summarizes the outcome of these bids.

Contractor	**Base Bid**
Michael Paul Company.	**$3,749,000**
OC Jones & Sons	$3,788,700
Ghillotti Brothers	$3,797,000
Sausal Corporation	

Observations

- Bid documents on projects bid and awarded during the 2010-11 audit period provided verification that the District sought competitive bids for construction contracts and equipment purchases for projects funded under the Measure D (2002) and J bonds and awarded projects to lowest responsive responsible bidders.

- The District has maintained the list of pre-qualified contractors to perform work for

CHANGE ORDER PROCEDURES

Objective

To gather data and review change order documents to verify that the processing of change orders

focus includes adherence to District design standards, ensuring that contractor-generated change orders and District-requested additions or changes are necessary and appropriate, and working to achieve the facility's designed programmatic efficiency for the facility's designed purpose. The Project Manager submits its recommendations to the Associate Superintendent for Operations for approval and

- Unforeseen conditions accounted for 16.78 percent of the cost of change orders for the projects examined during this period. The disposal of soil contaminated with hazardous materials (e.g., asbestos, petroleum products), hazardous demolition debris, and waste were the most common unforeseen conditions encountered during this period. Other

- The use of allowances to pay for additional costs reported in the above projects was consistent with the intended purposes of the allowances for each contract. However, in WKH SUHYLRXV \HDU¶V DXGLW 766 GLG QRW ILQG FK credited the remaining unused contract allowance back to the District for the Pinole Middle School New Building and Gymnasium Project. The project has since been completed and a Notice of Completion has been issued.

- Staff terminated the remaining phases of Verde and Lupine Hills Elementary Schools contracts due to changes in scope of work that will generate change orders in excess of Public Contract Code limits. Remaining phases of the work will be publicly bid and constructed.

Conclusion

- The District is in compliance with the requirements of Public Contract Code Section 20118.4a and b which sets the threshold for change orders at 10 percent of the contract amount.

Recommendation

- It is recommended that the District review change order documents for Pinole Middle School New Building and Gymnasium Project to verify that the remaining unused allowance for the project is credited back to the District. It is further recommended that contract allowances for all bond-funded construction contracts are properly tracked to ensure that unused allowances are properly credited back to the District prior to final payment and project close-out.

CLAIM AVOIDANCE PROCEDURES

Objective

In this section, TSS evaluates and reviews the procedures used to limit the number of claims filed against the District related to construction projects.

Disputes over the cost of those changes can also lead to claims. The first line of defense in this case is to have accurate documentation. However, even the best set of documents requires some clarification during construction. When a Request for Information (RFI) is issued by the contractor it is imperative that the issue be resolved quickly so that there is no cause for a delay claim. If a change order is required, decisions from the District should be rendered expeditiously to avoid additional delays. If the cost of the change cannot be agreed upon, a construction change directive (CCD) should be issued, instructing the contractor to proceed with the work while a cost is being negotiated.

Observations

- It was noted in the 2010 Performance Audit that two claims had been submitted during that audit period: West Coast Contractors and West Bay Contactors. Both claims were for additional costs due to project delays. After a delay consultant reviewed the West Coast claim, it was rejected by the District and no further action has been taken by the contractor. The West Bay claim was settled. No further claims were reported.

- The District has implemented a number of procedures to deal with and/or prevent potential claims. Several years ago, a Design Manager was contracted by the District to coordinate the work of the design teams and to assist in the process of ensuring that the documents were as accurate as possible. One of the responsibilities of the Design Manager is to perform constructability and coordination reviews of documents for each project. The comments from these reviews are incorporated into the documents. The result has been more accurate documentation and less opportunity for claims.

- To help with delay claims the District has implemented procedures that have shortened the time required for the approval of changes. On site project managers can now approve changes that do not exceed $5,000. All other change requests go before the Change Order Committee for review. The committee meets weekly to review change requests. The committee reviews the contractor generated change requests for validity and cost and they DUH DOVR UHYLHZHG IRU FRQIRUPDQFH ZLWK WKH generated change requests are reviewed for conformance with the project program, the 'LVWULFW¶V GHVLJQ VWDQGDUGV DQG LPSDFW RQ WKH

- The preconstruction review procedures established by the District provide the opportunity to reduce the number of changes required during construction and the number of potential claims on each project. Care should be taken to ensure that the comments to constructability and coordination reviews are reviewed thoroughly by the design teams and incorporated into the documents.

Conclusion

- The construction change review process established by the District has been effective in reducing the number of claims submitted by the contractors. Allowing on site managers to approve smaller changes results in shorter approval times and less opportunity for delay claims.

Recommendations

- The District should ensure that CPM schedules are submitted and updated in a timely manner as required by the contract documents as the primary tool in determining the validity of a delay claim.

- The District should endeavor to keep owner generated changes during construction to a

MEASURE J EXPENDITURES AND PAYMENT PROCEDURES

Objective

The objective of this performance audit section was to verify that the District was compliant with its policies and procedures related to Proposition 39 expenditures and payments.

Scope and Methodology

The scope of this performance audit section was to verify transactions of Measure J funds expended during the fiscal year ended June 30, 2011. During this period, only Measure J funds had financial activity as Measure D and Measure M funds were closed out in prior periods. TSS analyzed Measure J payment activities and compared the results to the Measure J bond language. TSS judgmentally selected Measure J expenditures for review, focusing on transactions with higher dollar amounts and higher audit risks, and verified that the funds were used in accordance with the taxpayer-approved purposes.

In the process of this performance audit, numerous purchasing and payment documents pertaining to expenditures funded by Measure J were reviewed. Interviews were held with District and SGI program management staff related to the payment policies and procedures for Measure J funds.

The audit consisted of the following:

- Verification that expenditures charged to the Measure J bond were authorized as Measure J projects;
- &RPSOLDQFH ZLWK WKH 'LVWULFW¶V SXUFKDVLQJ DQG
- Verification that backup documentation, including authorized signatures, were present on payment requests; and
- Determination that timely payments were made to vendors.

Background

$V SDUW RI WKH ERQG SURJUDP¶V GRFXPHQWDWLRQ SURFHVV WKH IROORZLQJ SURFHGXUHV DUH LQ SODFH DQG IROORZHG

- Requisitions are entered into the requisition workflow system and routed for approval in the following order:

- Approximately 95 percent of bond related invoices are mailed directly t R W K H ' L V W U L F V facilities office. SGI staff collects all invoices that are submitted directly to the District daily to ensure timely processing of vendor invoices.

- Once invoices are received for approved requisitions, SGI staff logs information into the invoice tracking/monitoring system.

- A payment history and payment approval form are prepared and routed for authorization signatures to designated individuals, which includes program controls (SGI), the Bond Program Manager (SGI), District Engineering Officer, District Principal Accountant for

TSS selected a sample of 33 checks that focused on vendors that collected more than $1,000,000 during the fiscal year ended June 20, 2011. In addition, TSS scanned the summary report of vendors paid for unusual activity and selected payments made to the Internal Revenue Service, Trust accounts, Law firms, and the E P S O R \ H U ¶ V $ G Y R F D W H , Q F 7 K H W R W D
was $24,943,060. TSS also made inquiries during their interviews with board members and District staff whether they were aware of complaints for delays in vendor payments.

Recommendations

- &XUUHQWO\ RQO\ WKH 'LVWULFW¶V ILQDQFH GHSDUWPHQW approves payments related to financial matters. Examples of checks reviewed by TSS were

and nationwide. This is accomplished through competitively bidding contracts for quality
S U R G X F W V W K U R X J K D U³ 0DH³DOGH SS EVOWLE WDHJ 1H Q F \´ R

- It was noted in prior performance audit reports that the Purchasing Department should have a more active role in the oversight of the procurement of equipment and/or supplies funded through bond proceeds. Helping to ensure that the District receives maximum value for items purchased and the procurement methods are in alignment with BP 3300 and Public Contract Code, it would also provide some relief to the Facilities Department, which operates with minimal staff.

Conclusion

- The results of this examination showed that the procurement methods utilized were in compliance with District policy and the requirements of Public Contract Code Sections 20111, 20118 and 22030 thru 22045.

To develop the construction documents, the Architect of Record held several meetings with various District departments during the design phase. Meetings were held with the Program Manager, the District Engineering Officer, District Maintenance personnel and other key stakeholders. At the meetings, the AOR, SGI staff and District personnel discussed key components for the project, the major systems to be included, and the CHPS goals to be implemented. The District and SGI staff reviewed construction documents and provided

Recommendations

- In the prior year's performance audit report 7 a formal process for updating the District's standards their product standards. Some previous standards are no longer valid simply due to the District adoption of CHPS goals. The District should update the standards, incorporating new CHPS goals, as soon as possible in the event that new green building products being specified may be too difficult to maintain or not compatible with existing systems. This may be difficult until some CHPS related products are installed and evaluated. For example, metal wall panels for some building exterior walls were specified on the Nystrom project although maintenance staff typically prefers stucco. The new metal wall panels can be made of recycled products and provide other aesthetic or CHPS-related benefits; however the different systems have entirely different maintenance needs.

- The building specifications, in general, were open to multiple products versus sole-sourced products. However, to achieve CHPS goals, some of the technical specifications only allowed for one manufacturer's product V sourcing can lead to higher bid prices If possible should be allowed even for systems designed around CHPS criteria. It is recognized that this may be difficult due to the limited number of green building products currently on the m4<005<005<005<005<005<005<005<005<005<005<005<<00-99(gr)3(e)4(*7<005i)-13(ons,)-250

DELIVERED QUALITY ±Comparison of Design Standards and Installed Products
Dover Elementary School New Construction Increment II

Product/System	Specification Section	Initial Criteria	Specified	Submittal Status	Comment

Product/System	Specification Section	

Product/System	Specification Section	Initial Criteria	Specified	Submittal Status			Comment
				Approved	Rejected	Pending	
Carpeting	9688	Meet CHPS criteria					

SCOPE, PROCESS, AND MONITORI

- Portola Middle School Temporary Campus, Fencing and Drainage
- Richmond High School Arts Building Fire and Intrusion Alarm Project
- Stewart Elementary School Restroom Resurfacing

As of June 30, 2011, eighteen (18) of the twenty-five (25) above noted projects were under

Project Labor Agreement Update

In September 2011, the Governor signed SB922 which authorizes public agencies to enter into, and to require contractors to enter into, project labor agreements prior to awarding a contract for construction of a public works project to avoid delays and interruptions to construction caused by strikes, lockouts or work stoppages. Because PLAs have been the subject of controversy and litigation for some public agencies, SB922 codified the legality of these agreements and places certain restrictions and requirements as to the terms. Project Labor Agreements on public works projects are now expressly permitted under California law, thus eliminating some of the uncertainty and controversy that has surrounded them. However, all project labor agreements PXVW LQFOXGH ILYH ³WD[SD\HU SURWHFWLRQ SURYLVLRQV´

(1) The agreement prohibits discrimination based on race, national origin, religion, sex, sexual orientation, political affiliation or membership in a labor organization in hiring and dispatching workers for the project;

(2) The agreement permits all qualified contractors and subcontractors to bid for and be awarded work on the project without regard to whether they are otherwise parties to collective bargaining agreements;

(3) The agreement contains an agreed-upon protocol concerning drug testing for workers who will be employed on the project;

(4) The agreement contains guarantees against work stoppages, strikes, lockouts, and similar disruptions of the project; and

(5) The agreement provides that disputes arising from the agreement shall be resolved by a neutral arbitrator.

EFFECTIVENESS OF THE COMMUNICATION CHANNELS AMONG ALL STAKEHOLDERS WITHIN THE BOND PROGRAM

Objective

7KH REMHFWLYH RI WKLV VHFWLRQ LV WR GHWHUPLQH WKH
the Bond Program and progress to community members and stakeholders.

Scope and Methodology

To meet the objective, all avenues of communication, including public presentations at Board meetings, CBOC activities, District website postings, newsletters and billboards were considered. During the process of this examination, Total School Solutions interviewed Board PHPEHUV PHPEHUV RI WKH &LWL]HQV¶ %RQG 2YHUVLJ
Communication channels and public outreach were among the topics of discussion in these interviews.

The bond program website, which was updated significantly during 2010-11, has been improved to include links to each school with an active Bond program project; plans, budget information and reports, pictures or presentations, as well as current information about all construction projects and relevant information about upcoming projects is included. Information about the organizational structure and personnel providing oversight and management of the program is also included.

Board members and CBOC members interviewed during the course of this review indicated that coverage by local media regarding the activities at the District and the Bond program are

Meeting Date	Members/Alternates In Attendance	Members Absent	Quorum
July 28, 2010[1]	9	unknown	unknown
August 25, 2010	7	4	Yes
September 22, 2010	9	5	Yes
December 15, 2010	10	6	Yes
January 26, 2011	15	5	Yes
February 23, 2011	13	8	Yes
March 23, 2011	14	6	Yes
April 27, 2011	13	7	Yes

Observations

- Meeting minutes from the July 28, 2010, August 25, 2010, September 22, 2010, October 27, 2010 and November 10, 2010 meetings were not approved until the January 26, 2011 meeting of the CBOC. The meeting minutes from the December 15, 2010, January 26, 2011, and March 23, 2011 meetings were not approved until the meeting on April 27, 2011. These lengthy delays in approval and subsequent posting of approved minutes results in a failure by the CBOC to provide timely information to the public about the use of bond proceeds and the related activities in the bond program.

- It appears that the delay in meeting minute approval was related to a lack of approved guidelines for minute taking and recording. Therefore, lengthy discussions related to the

Recommendation

- The content and format of meeting minutes is one of the most critical aspects of a meeting, especially D SXEOLF PHHWLQJ 7KHUH LV QR VWDQGDU bond oversight committees however there are basic guidelines which TSS recommends the WCCUSD CBOC should utilize to establish a format that will provide an accurate and objective summary record of the important matters discussed at each meeting. The basic guidelines are as follows:

    - Name of the Group/Organization
    - Name of the Meeting, Address, Venue
    - Designations and names of participants, presenters, speakers and attendees
    - Time of meeting commencement
    - Agenda Items, including purpose (e.g., information, action, etc.)
    - Decisions/Motions (i.e., short, transparent statements)
    - Carry Forwards (e.g., issues to be tabled until later time/meeting)
    - Time of meeting conclusion

Committee Membership

The CBOC for Measures M, D, and J (Proposition 39 bonds) had, as of June 30, 2011, 21 designated membership positions with the following categories, exceeding the mandatory minimum seven members:

Statutory Requirements	5
City Council Representatives	5
Unincorporated Area Representatives	2
Board of Education Representatives	5
Council of Industries	1
Building Trades	1
Public Employees Union Local 1	1
CAC on Special Education	1
Total Membership	21

During the period from July 1, 2010 through June 30, 2011, CBOC membership, as reported in meeting minutes, ranged from a low of 11 members as of August 25, 2010, to a high of 21 members as of February 23, 2011, as the Board appointed members to fill vacancies. For the last meeting during the audit period, June 22, 2011, the CBOC minutes reported 20 members.

Based upon the revised BP 7214.2 discussed above, the Council of Industries membership and the CAC on Special Education membership was dropped.

Education Code Sect

CBOC Website

7KH &%2& PDLQWDLQV D ZHEVLWH ZLWK D OLQN IURP WKH

DISTRICT PROVIDED INFORMATION

The information on the succeeding pages was compiled by TSS staff from a District source and/or provided by District staff or consultants for informational purposes only. The information provided here has not been audited.

FACILITIES PROGRAM HISTORY/STATUS

7R DVVLVW WKH FRPPXQLW\ LQ XQGHUVWDQGLQJ RI WKH 'LVW Chronology of events and/or decisions that resulted in the increased scopes and costs for projects, this report documents the events that have taken place since July 1, 2010. For a discussion of prior Board agenda items and actions, refer to earlier annual and midyear reports. Major actions of the Board of Education are listed in the table below.

Chronology of Facilities Board Agenda; July 1, 2010 thru June 30, 2011.

DATE	ACTION	AMOUNT
July 7, 2010 (Consent Item # C.11)	Ratification and approval of Engineering Services Contracts.	$617,627
July 7, 2010 (Consent Item # C.12)	Ratification and approval of Negotiated Change Orders.	$86,526
July 7, 2010 (Consent Item # C.13)	Approve Construction Access, Right of Use and Restoration License Agreement with t	

DATE	ACTION	AMOUNT
July 28, 2010 (Consent Item # C.24)	$SSURYDO RI $SSRLQWPHQWV WR WKH &LW (CBOC) ; x Jason Gallia - (New) representing Contra Costa Building Trades Council x Marcus Mitchell - (Re-appointment) representing Public Employees Union Local 1	
July 28, 2010 (Action Item # F.2)	$SSURYH SURFHHGV IURP 0HDVXUH ³-´ 6HU	

DATE	ACTION	AMOUNT
	Special Education.	
October 6, 2010 (Consent Item # C.16)	Ratification and approval of Negotiated Change Orders	$116,640
October 6, 2010 (Consent Item # C.17)	Ratification and approval of Engineering Services Contracts	

DATE	ACTION	AMOUNT
January 5, 2011 (Consent Item # C.11)	$ S S U R Y D O R I $ S S R L Q W P H Q W V W R W K H & L W (CBOC) ; X	

DATE	ACTION

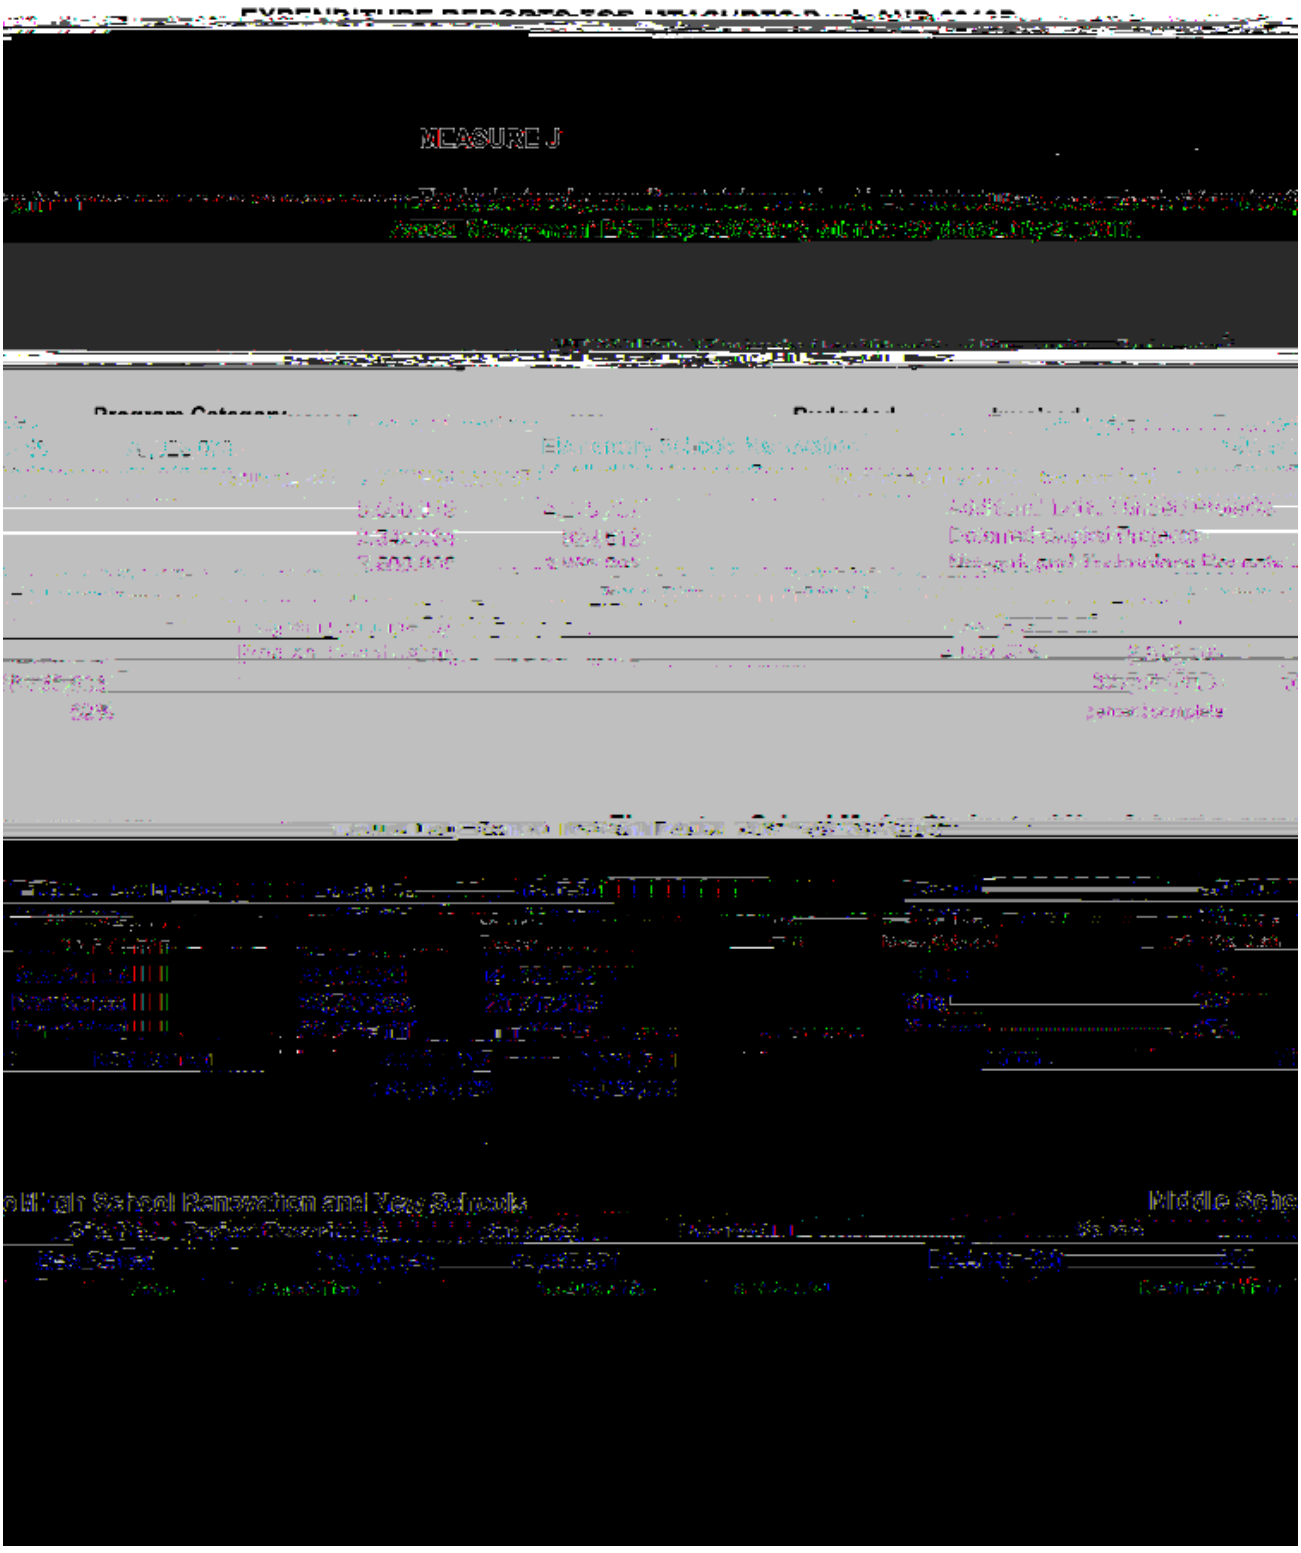
MEASURE J

Deferred Capital Projects

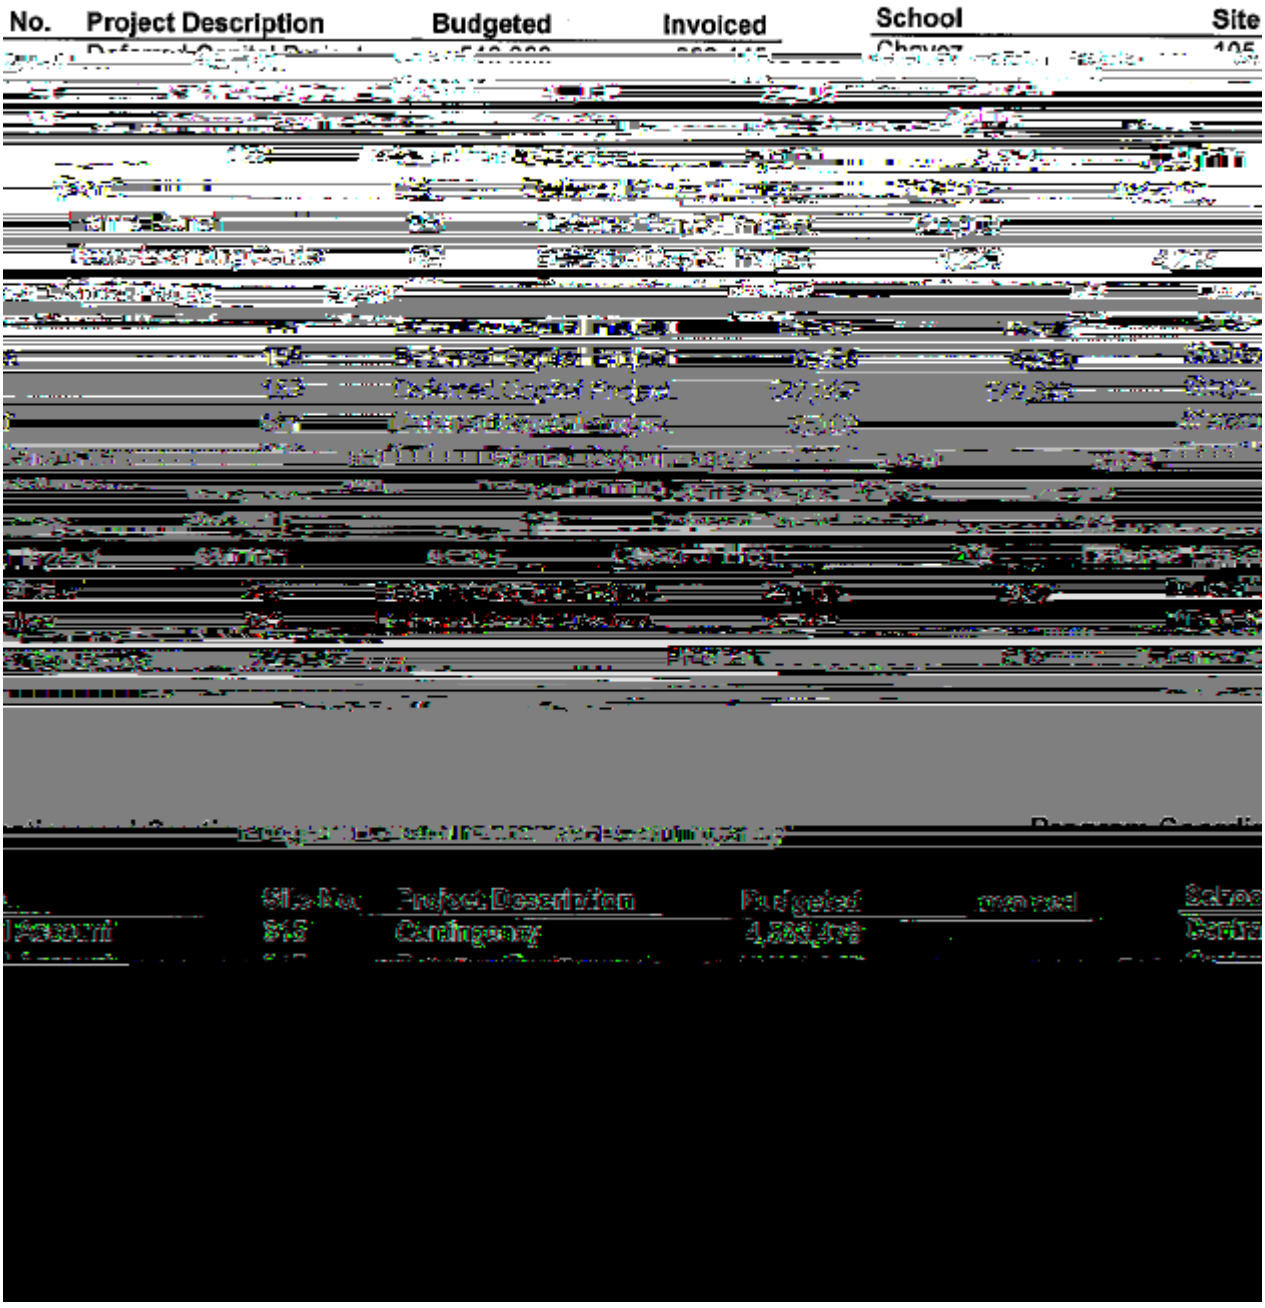

No.	Project Description	Budgeted	Invoiced	School	Site
				Chavez	105

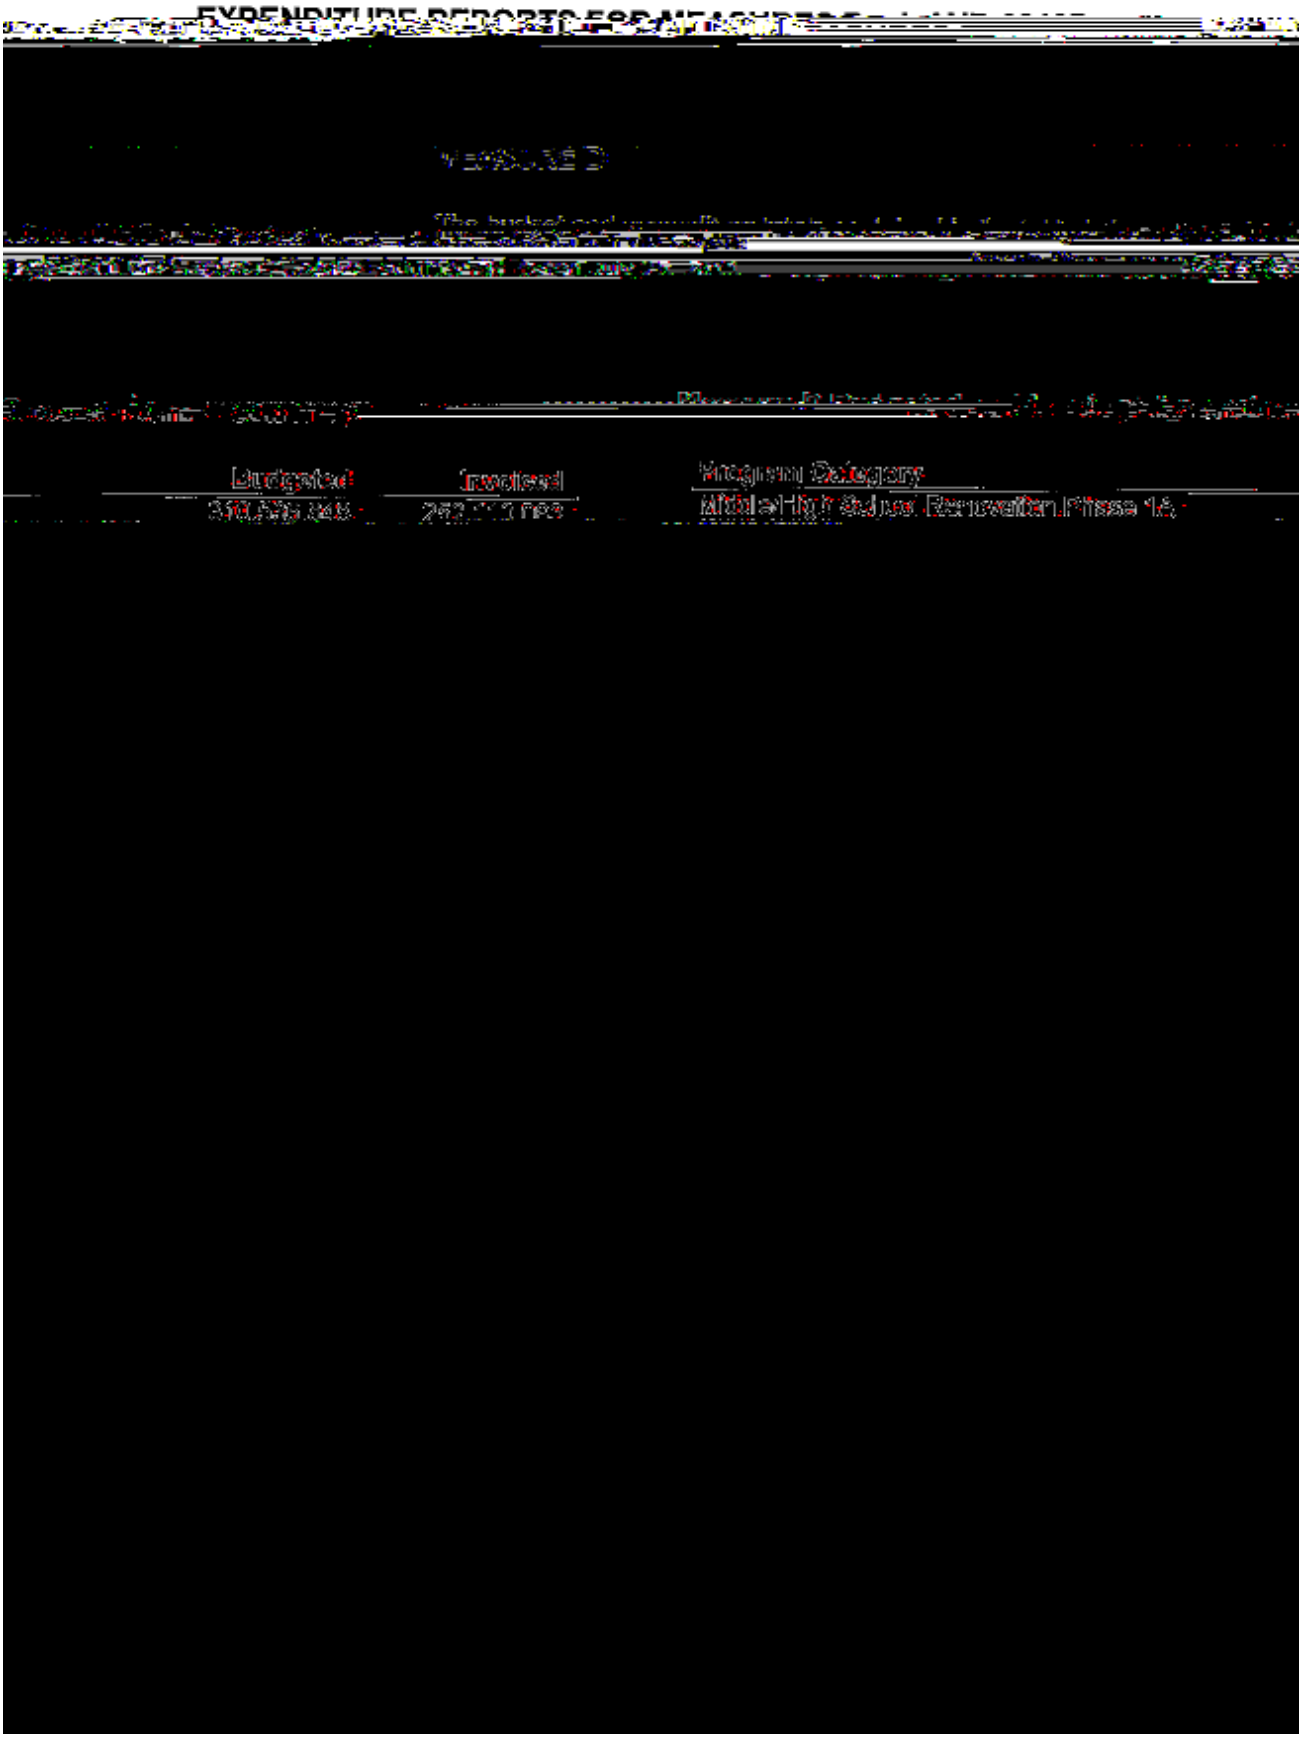
Budgeted
Invoiced
Program Category
Middle/High School Renovation Phase 1A

DISTRICT FACILITIES PROGRAM ±A PERSPECTIVE

Facilities Program ±Financial Status (in thousands)

	Fiscal Year (as of June 30 for each Fiscal Year) in thousands										
Source	**2000-01**	**2001-02**	**2002-03**	**2003-04**	**2004-05**	**2005-06**	**2006-07**	**2007-08**	**2008-09**	**2009-10**	**2010-11**
Bonds Outstanding[1]	$54,340	$122,450	$216,455	$315,155	$380,634	$544,027	$536,504	$527,016	$636,220	$758,223	$741,277
Developer Fees Revenues[2]	6,061	2,750	9,094	10,499	7,760	8,813	4,840	2,374	813	652	152
Developer Fees Ending Balance	3,526	1,294	8,928	21,038	27,534	34,162	10,730	4,910	4,869	4,725	3,468
State School Facilities Program New Construction Revenues[3]	None	None	12,842	None	None	None	None	None	None	571	None
State School Facilities Program Modernization, Emergency Repair Program and Joint-											

CAPITAL FACILITES FUNDS

Fiscal Year Ending June 30, 2009	Fund 14 Deferred Maint. Fund[1]	Fund 21 Building Fund[2]	Fund 25 Capital Facilities

'XULQJ WKLV DXGLW SHULRG LQ D UHSRUW SUHSDUHG E\ W
December 9, 2010, actual 2010-11 tax rates per $100,000 of A/V were the following:

Measure E (1998)	$11.30
Measure M (2000)	$55.60
Measure D (2002)	$60.00
Measure J (2005)	$60.00
Total	**$186.90**

Investment of Bond Proceeds

The proceeds from bond sales are invested in various instruments and earn interest until expenditures DUH PDGH 7KH 'LVWULFW¶V Fiscal Agent for the fiscal year ended June 30, 2011, reports the following cash investments:[1]

Pooled Funds (Cash in County Treasury)	$65,960,325
Cash with Fiscal Agent	$7,935,590
Investments-Local Agency Investment Fund (LAIF)	$67,873,504
Total	$141,769,419

[1] West Contra Costa Unified School District, Financial Statements with Supplementary Information for the Year Ended June 30, 2011, Crowe Horwath, LLP, Accountants, December 7, 2011.

Pooled Funds are short-WHUP LQYHVWPHQWV PDGH E\ &RQWUD &RVWD earnings are credited quarterly. The District has no control over the investments, and its risk/return is based on the investment decisions of the County Treasurer. The financial auditor reported that, as of -XQH WKH SRROHG IXQG ³FRQWDLQHG QR GHULYDWLYH SURILOHV ´

&DVK ZLWK)LVFDO $JHQW UHSUHVHQWV FRQWUDFW UHWH independent third party, and the contractor carries all investment risk. As contract payments are made, ten percent is retained until the completion of the contract. The contractor may request to deposit the retention amount with a Fiscal Agent in an interest-bearing account. After a Notice of Completion is filed and all claims resolved, the retention including any earned interest is released to the contractor.

LAIF investments are under the oversight of the Treasurer of the State of California, and consist of pooled funds of governmental agencies. LAIF investments generally have a higher risk/return than local pooled funds and are generally longer-term investments.

By utilizing county and state pooled funds, the bond proceeds earn low-risk interest from the time the bonds are sold until proceeds are expended. Pooled funds with the County are immediately accessible by the District to meet its cash-flow needs. Funds in the LAIF require District action to withdraw. The combination of local and state pooled funds is a sound investment approach to maximize interest earnings between the time the bonds are sold and the funds are expended.

Deferred Capital Project Fund

On February 20, 2009, SBX3 4 was signed into law, providing school districts budgeting flexibility. One of the provisions of SBX3 4 impacted the Deferred Maintenance Program by eliminating the local matching contribution for the years 2008-09 through 2012-13 and by making funding for deferred maintenance flexible by allowing such funds to be used for educational purposes.

The West Contra Costa Unified School District utilized the above provisions of SBX3 4 related to the Deferred Maintenance Program on March 6, 2009 to transfer funds in reserve within the Deferred Maintenance Fund to the District's Class Size Reduction Program. As of June 30, 2010, $4.0 million of Deferred Maintenance Fund reserves were transferred to the General Fund, Tier III, leaving a $1.1 million reserve in the Deferred Maintenance Fund.

As a result of the Board's actions a Deferred Capital Projects Fund. On April 14, 2010, the Board approved Measure J bond program budget adjustments which included a $2,342,234 allocation to the Deferred Capital Projects fund for the stated purpose to support capital maintenance expenditures District-wide.

Arbitrage

When a school district issues general obligation bonds, the investments are subject to arbitrage regulations set forth by the United States Department of the Treasury. The bonds are subject to an allowable yield on investments which, if exceeded, results in a rebate liability that would be owed to

STATE NEW CONSTRUCTION STATUS

NOTICE OF ELECTION AND THE NOTICE

FIXING AUGUST 15, 2000 AS FINAL DATE TO SUBMIT ARGUMENTS

ON THE WEST CONTRA COSTA UNIFIED SCHOOL DISTRICT BOND MEASURE

AT ELECTION ON TUESDAY, NOVEMBER 7, 2000

NOTICE IS HEREBY GIVEN that a Bond Measure Election will be held in West Contra Costa Unified School District, Tuesday, November 7, 2000.

NOTICE IS ALSO HERBY GIVEN by the County Clerk of Contra Costa court, Pursuant to Elections Code Section 9502 that the above date is hereby fixed as the final date on which arguments for and against the following measure appearing on the ballot may be submitted to the County Clerk at 524 Main Street, Martinez, California 94553, for printing and distribution to the voters as provided by law.

To improve the learning climate for children and relieve overcrowding by improving elementary schools through building classrooms, repairing and renovating bathrooms, electrical, plumbing, heating and ventilation systems, leaking roofs and fire safety systems, improving technology, making seismic upgrades, and replacing deteriorating portable classrooms and buildings, shall the West Contra Costa Unified School District issue $150,000,000 in bonds at authorized rates, to

APPENDIX B

MEASURE D (2002) BOND LANGUAGE

BOND MEASURE D
WEST CONTRA COSTA UNIFIED SCHOOL DISTRICT

3 7R FRPSOHWH UHSDLULQJ DOO RI RXU VFKRROV LPSURYH through such projects as: building additional classrooms; making seismic upgrades; repairing and renovating bathrooms, electrical, plumbing, heating and ventilation systems, leaking roofs, and fire safety systems; shall the West Contra Costa Unified School District issue $300 million in bonds at authorized interest rates, to renovate, acquire, construct and modernize school facilities, DQG DSSRLQW WHDUHV WKLV LQGHSHQGHQW RYHUVLJKW DQG DXGLW

FULL TEXT OF BOND MEASURE D

BOND AUTHORIZATION

By approval of this proposition by at least 55% of the registered voters voting on the proposition, the West Contra Costa Unified School District shall be authorized to issue and sell bonds of up to $300,000,000 in aggregate principal amount to provide financing for the specific school facilities projects listed in the Bond Project List attached hereto as Exhibit A, and in order to qualify to receive State matching grant funds, subject to all of the accountability safeguards specified below.

proceeds of the bonds re

TAX RATE STATEMENT IN CONNECTION WITH

BOND MEASURE D

An election will be held in the West Contra Costa Unified School District W K Dis t ´ R Q March 5, 2002, to authorize the sale of up to $300,000,000 in bonds of the District to finance school facilities as described in the proposition. If the bonds are approved, the District expects to sell the bonds in 7 series. Principal and interest on the bonds will be payable from the proceeds of tax levies made upon the taxable property in the District. The following information is provided in compliance with Sections 9400-9404 of the Elections Code of the State of California.

1. The best estimate of the tax which would be required to be levied to fund this bond issue during the first fiscal year after the sale of the first series of bonds, based on estimated assessed valuations available at the time of filing of this statement, is 1.22 cents per $100 ($12.20 per $100,000) of assessed valuation in fiscal year 2002-03.

2. The best estimate of the tax rate which would be required to be levied to fund this bond issue during the first fiscal year after the sale of the last series of bonds, based on estimated assessed valuations available at the time of filing of this statement, is 5.94 cents per $100 ($59.40 per $100,000) of assessed valuation in fiscal year 2010

pet484.0eET in

Exhibit A

WEST CONTRA COSTA UNIFIED SCHOOL DISTRICT
BOND PROJECT LIST

SECTION I

PROJECTS TO BE COMPLETED AT ALL SCHOOL SITES
(As needed, upon final evaluation of each site.)

Security and Health/Safety Improvements

- Modifications and renovations necessary for compliance with Americans with Disabilities Act (ADA).
- Improvements required for compliance with applicable building codes including the Field Act.
- Remove, abate, or otherwise mitigate asbestos, lead-based paint and other hazardous materials, as necessary.
- Install closed circuit television (CCTV) systems, as necessary, to provide secure environment for students, staff, and other users of the facilities.
- Survey, assess and mitigate seismic and structural issues and reinforce or replace existing structures, as necessary, except at Hercules Middle/High School and Richmond Middle School.
- Purchase necessary emergency equipment and provide adequate storage for such equipment.

Major Facilities Improvements

-

- x Replace doors, hardware, windows and window coverings.
- x Create, renovate and/or improve kitchen areas, including replacement of specialized equipment and furnishings.
- x Renovate, upgrade or install library areas, including seismic restraints for shelving.
- x Renovate, improve or replace restrooms.
- x Renovate, improve or replace roofs.
- x Re-finish and/or improve exterior and interior surfaces, including walls, ceilings, and floors.
- x Upgrade, improve, install and/or replace indoor lighting systems.
- x Provide furnishings and equipment for improved or newly constructed classrooms and administrative facilities.
- x Replace worn/broken/obsolete instructional and administrative furniture and equipment, as well as site furnishings and equipment.
- x Purchase, rent, or construct temporary classrooms and equipment (including portable buildings) as needed to house students displaced during construction.
- x Acquire any of the facilities on the Bond Project List through temporary lease or lease-purchase arrangements, or execute purchase options under a lease for any of these authorized facilities.
- x Construct regional School District Maintenance and Operations Yard or Yards at current District locations as necessary.
- x As to any major renovation project, replace such facility if doing so would be economically advantageous.

<u>Sitework</u>

- x

PROJECT TYPE	**Portola Middle School** 1021 Navellier Street, El Cerrito, CA 94530-2691 **Project List**
	3URMHFWV DV DSSURSULDWH IU
Improvements/Rehabilitation	Replace interior and exterior doors. Improve and paint interior walls. Improve/replace ceilings. Improve/replace floor surfaces. Improve/replace overhangs. Replace ceilings and skylights in 400 wing. Replace glass block at band room. Improve/replace concrete interior walls at 500 wing. Eliminate dry rot in classrooms and replace effected materials. Replace walkways, supports, and overhangs outside of 400 wing.
Construction/Renovation of Classroom and Instructional Facilities	Construct/install restrooms for staff. Renovate 500 wing. Reconfigure/expand band room.
Site and Grounds Improvements	Improve and expand parking on site.
Furnishing/Equipping	Install

Site and Grounds Improvements	Improve/replace fence around perimeter of school.
Furnishing/Equipping	Install or replace whiteboards, tackboards and counters. Improve/replace hydraulic lift in auto shop. Replace pullout bleachers in gymnasiumift in auto shop.

PROJECT TYPE	**Vista Alternative High School** 2600 Moraga Road, San Pablo, CA 94806 **Project List**
	3URMHFWV DV DSSURSULDWH IU
Major Building Systems Construction/Renovation of Classroom and Instructional Facilities	Add water supply to portable classrooms. Add storage space. Add mini-

APPENDIX C

MEASURE J (2005) BOND LANGUAGE

WEST CONTRA COSTA UNIFIED SCHOOL DISTRICT
Resolution No. 25-0506

RESOLUTION OF THE BOARD OF EDUCATION OF THE WEST CONTRA COSTA UNIFIED SCHOOL DISTRICT ORDERING A SCHOOL BOND ELECTION, AND AUTHORIZING NECESSARY ACTIONS IN CONNECTION THEREWITH

: + (5 ($ 6 W K H % R D U G R I (G X F D W L R Q W K H : H V W & R Q W U D & R V W D 8 Q L I L H G 6 F K R R O R I W K H District W K L V ´ Z L W K L Q W K H & R X Q W \ R I & R Q W U D & R V W D authorized to order elections within the

Section 1. Specifications of Election Order. Pursuant to sections 5304, 5322, 15100 et seq. and section 15266 of the California Education Code, an election shall be held within the boundaries of the West Contra Costa Unified School District on November 8, 2005, for the purpose of

appropriate annual period as the Superintendent shall determine, and may be incorporated into the annual budget, audit, or other appropriate routine report to the Board.

BOND PROJECT LIST

The Bond Project List attached to this resolution as Exhibit A shall be considered a part of the ballot proposition, and shall be reproduced in any official document required to contain the full statement of the bond proposition. The Bond Project List, which is an integral part of this proposition, lists the specific projects the West Contra Costa Unified School District proposes to finance with proceeds of the Bonds. Listed repairs, rehabilitation projects and upgrades will be completed as needed. Each project is assumed to include its share of costs of the election and bond issuance, architectural, engineering, and similar planning costs, construction management, and a customary contingency for unforeseen design and construction costs. The final cost of each project will be determined as plans are finalized, construction bids are awarded, and projects are completed. In addition, certain construction funds expected from non-

Section 3.

any and all things that they deem necessary or advisable in order to effectuate the purposes of this resolution.

Section 11Effective Date. This Resolution shall take effect upon its adoption.

PASSED AND ADOPTED this day, July 13, 2005, by the following vote:
AYES:
NAYS:
ABSTAIN:
ABSENT:
APPROVED:

President of the Board of Education of the West Contra Costa Unified School District

Attest:

Clerk of the Board of Education of the West Contra Costa Unified School District

&/(5.¶6 &(57,),&$7(

I, Clerk of the Board of Education of the West Contra Costa Unified School District, of the County of Contra Costa, California, hereby certify as follows:

The attached is a full, true and correct copy of a resolution duly adopted at a meeting of the Board of Education of the District duly and regularly held at the regular meeting place thereof on

RECONSTRUCTION PROJECTS

The following projects will be completed as part of the reconstruction program of the District, as funds allow. The reconstruction program includes the following:

Health and Life Safety Improvements
Code upgrades for accessibility
Seismic upgrades
Systems Upgrades
Electrical
Mechanical
Plumbing
Technology
Security
Technology Improvements
Data
Phone
CATV (cable television)
Instructional Technology Improvements
Whiteboards
TV/Video
Projection Screens

In addition, the reconstruction program includes the replacement of portable classrooms with permanent structures, the improvement or replacement of floors, walls, insulation, windows, roofs, ceilings, lighting, playgrounds, landscaping, and parking, as required or appropriate to meet programmatic requirements and depending on the availability of funding.

PROJECT SCOPE

De Anza High School Reconstruction/New Construction
Kennedy High School Reconstruction/New Construction
Pinole Valley High School Reconstruction/New Construction
Richmond High School Reconstruction
Castro Elementary School Reconstruction
Coronado Elementary School Reconstruction
Dover Elementary School Reconstruction
Fairmont Elementary School Reconstruction
Ford Elementary School Reconstruction
Grant Elementary School Reconstruction
Highland Elementary School Reconstruction
King Elementary School Reconstruction
Lake Elementary School Reconstruction
Nystrom Elementary School Reconstruction
Ohlone Elementary School Reconstruction/New Construction
Valley View Elementary School Reconstruction
Wilson Elementary School Reconstruction

RESOLUTION NO. 76-0910

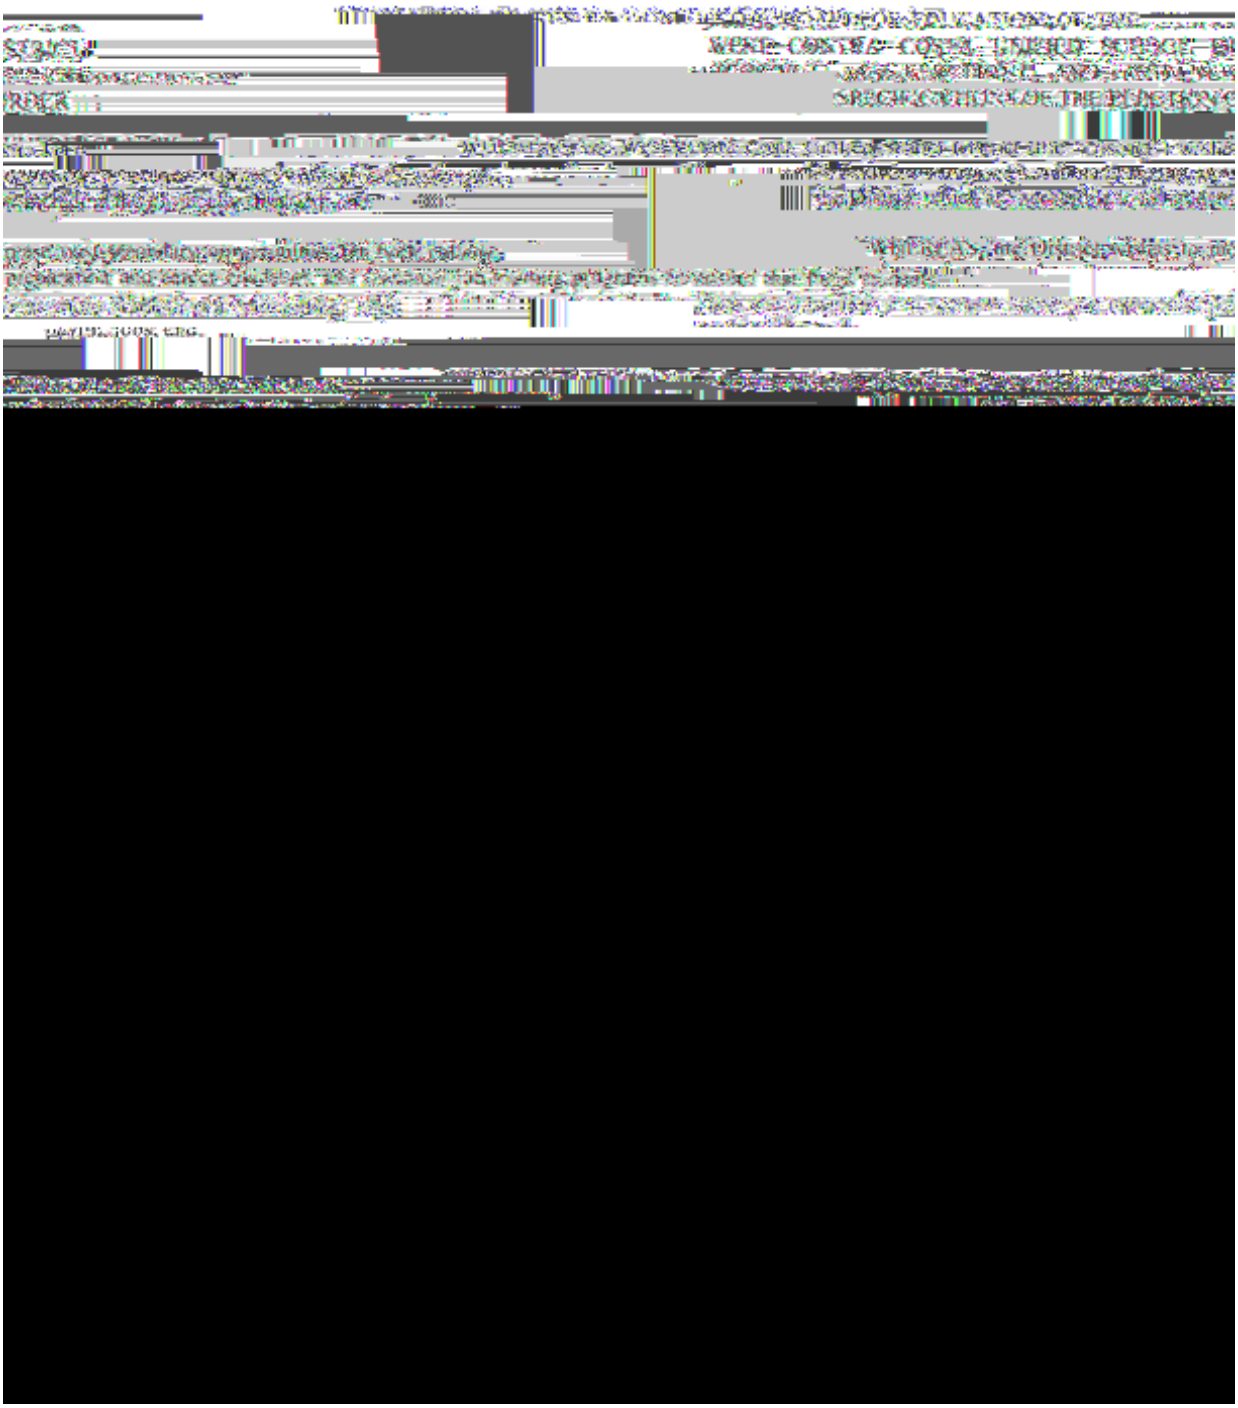

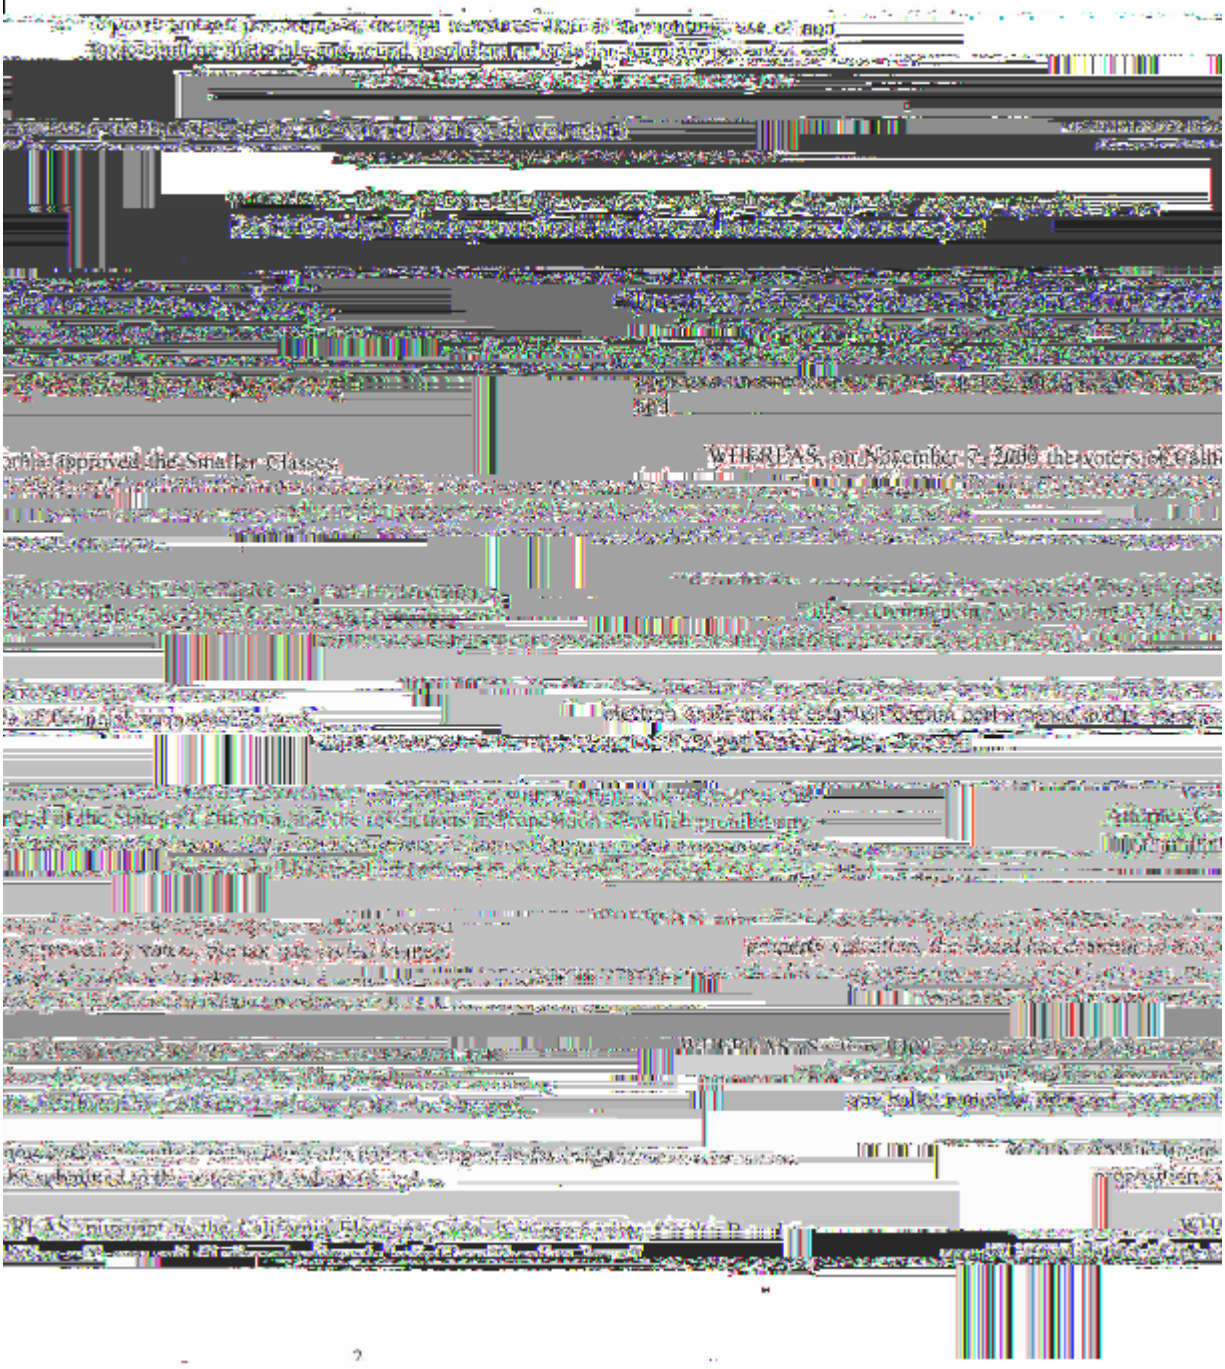

2010, and to request that the Contra Costa County Registrar of Voters perform certain election services for the District;

NOW THEREFORE, THE BOARD OF EDUCATION OF THE WEST CONTRA COSTA

AS FOLLOWS:

Section 1. The Board requests the Contra Costa

Section 2. That the date of the election shall be June 8, 2010.

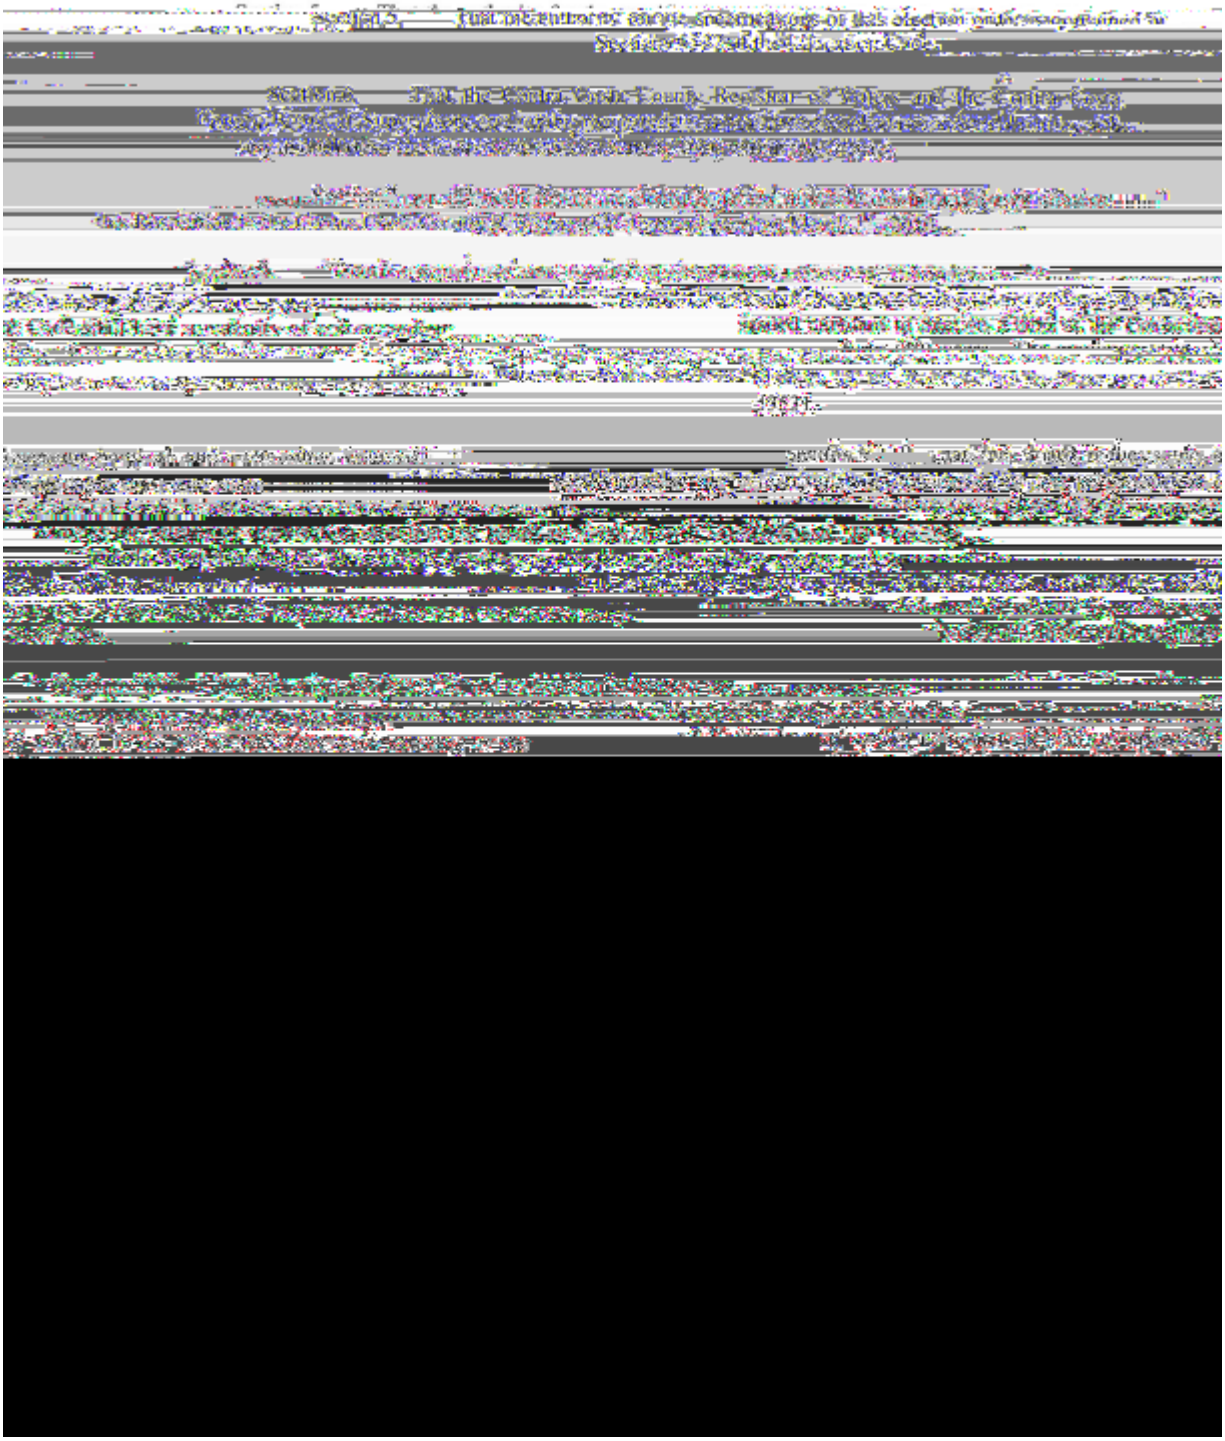

EXHIBIT B

FULL TEXT BALLOT PROPOSITION
OF TEXT
its schools should be safe learning environments, free from gang or drug
facilities should help the local economy by creating
businesses.
buildings and classrooms, priority shall be given to basic
outdated plumbing, piping, electrical
etc.
construction jobs for local
repairs, such as replac

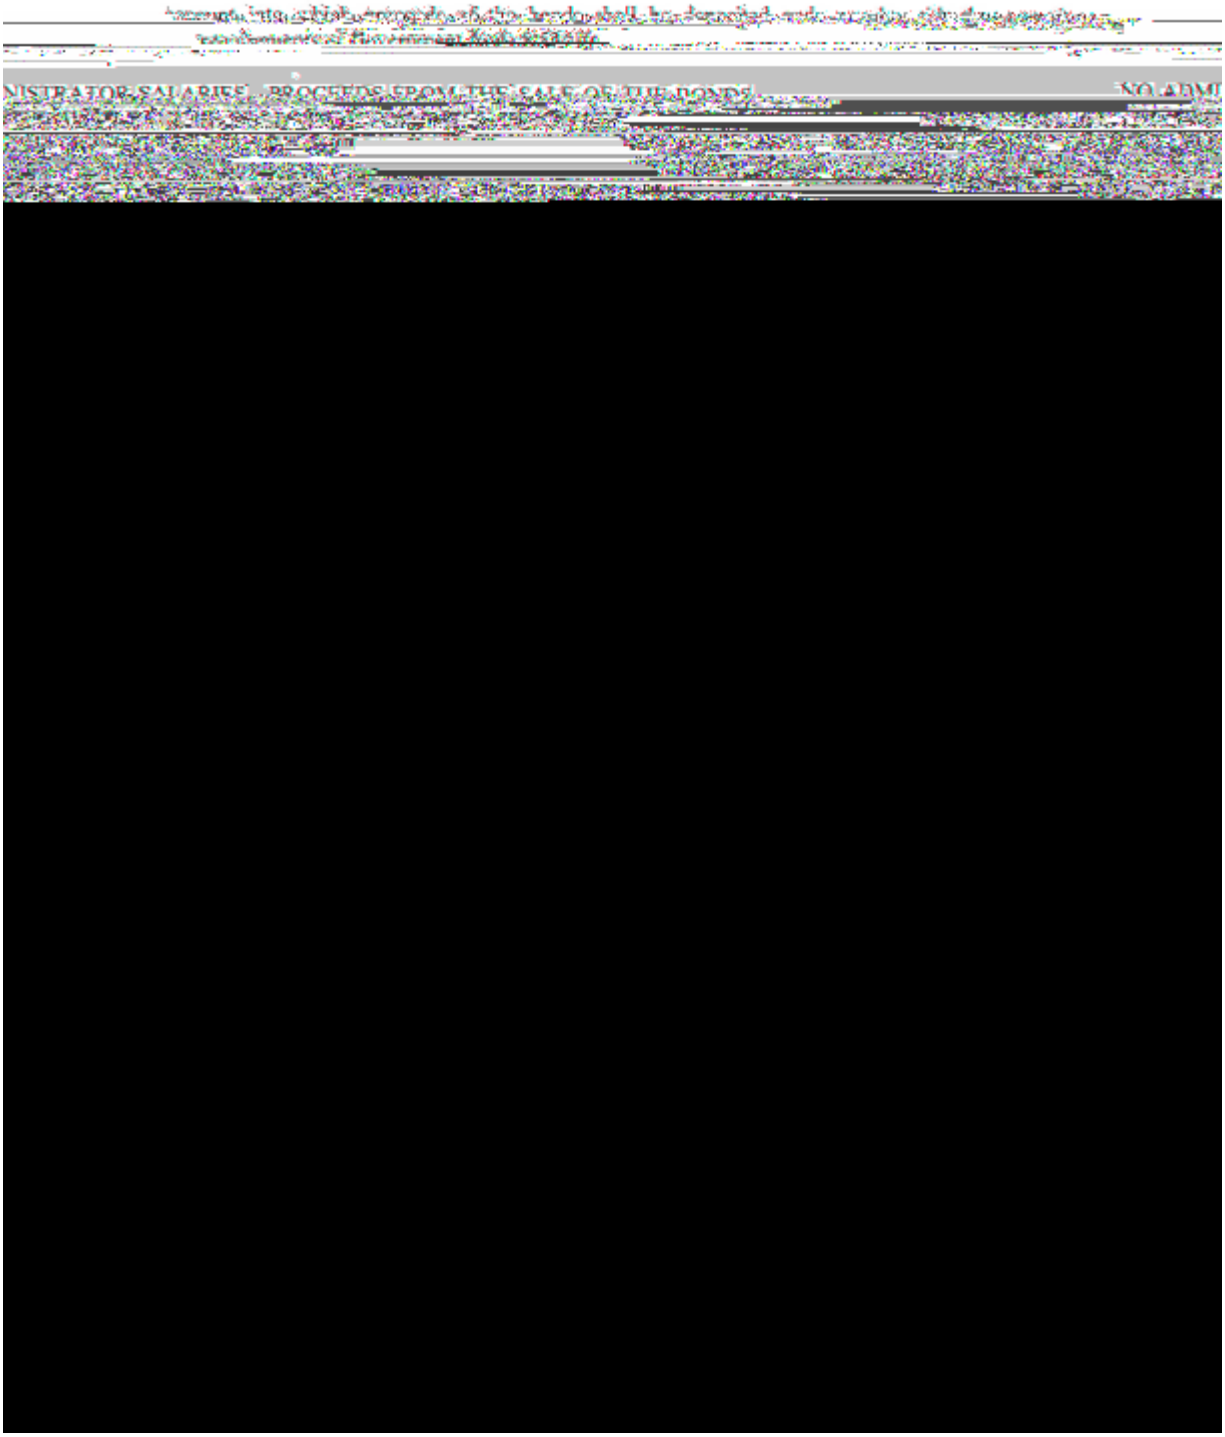

APPENDIX E

&,7,=(16¶ 29(56,*+7&200,77((

- Require mandatory independent training for bond oversight committee members. The State Allocation Board and the California Community Colleges should develop and host a Web site with easy-to-access training materials and easy-to-understand descriptions of the roles and responsibilities of t K H O R F D O F L W L] H Q V ¶ R Y H U V L J K W F F Web site should include a mandatory online training course.

- Require civic groups to nominate local committee members, allowing veto power for the school or community college district.

- Clearly delineate the role and responsibility of the local oversight committees and define the purpose and objectives of the annual financial and performance audits.

- Encourage county grand juries to review the annual financial and performance audits of expenditures from local school and community college bond measures.

- Impose sanctions for school and community college districts that fail to adhere to

15278. (a) If a bond measure authorized pursuant to paragraph (3) of subdivision (b) of Section 1 of Article XIII A of the California Constitution and subdivision (b) of Section 18 of Article XVI of the California Constitution is approved, the governing board of the school district or community college shall establish and appoint members to an independent citizens' oversight committee, pursuant to Section 15282, within 60 days of the date that the governing board enters the election results on its minutes pursuant to Section 15274.

(b) The purpose of the citizens' oversight committee shall be to inform the public concerning the expenditure of bond revenues. The citizens' oversight committee shall actively review and report on the proper expenditure of taxpayers' money for school construction. The citizens' oversight committee shall advise the public as to whether a school district or community college district is in compliance with the requirements of paragraph (3) of subdivision (b) of Section 1 of Article XIII A of the California Constitution. The citizens' oversight committee shall convene to provide oversight for, but not be limited to, both of the following:

(1) Ensuring that bond revenues are expended only for the purposes described in paragraph (3) of subdivision (b) of Section 1 of Article XIII A of the California Constitution.

(2) Ensuring that, as prohibited by subparagraph (A) of paragraph (3) of subdivision (b) of Section 1 of Article XIII A of the California Constitution, no funds are used for any teacher or administrative salaries or other school operating expenses.

(c) In furtherance of its purpose, the citizens' oversight committee may engage in any of the following activities:

(1) Receiving and reviewing copies of the annual, independent performance audit required by subparagraph (C) of paragraph (3) of subdivision (b) of Section 1 of Article XIII A of the California Constitution.

(2) Receiving and reviewing copies of the annual, independent financial audit required by subparagraph (C) of paragraph (3) of subdivision (b) of Section 1 of Article XIII A of the California Constitution.

(3) Inspecting school facilities and grounds to ensure that bond revenues are expended in compliance with the requirements of paragraph (3) of subdivision (b) of Section 1 of Article XIII A of the California Constitution.

(4) Receiving and reviewing copies of any deferred maintenance proposals or plans developed by a school district or community college district, including any reports required by Section 17584.1.

(5) Reviewing efforts by the school district or community college district to maximize bond revenues by implementing cost-saving measures, including, but not limited to, all of the following:

(A) Mechanisms designed to reduce the costs of professional fees.

(B) Mechanisms designed to reduce the costs of site preparation.

(C) Recommendations regarding the joint use of core facilities.

(D) Mechanisms designed to reduce costs by incorporating efficiencies in school site design.

(E) Recommendations regarding the use of cost-effective and efficient reusable facility plans.

APPENDIX F

GLOSSARY OF TERMS AND ACRONYMS

DTSC	**Department of Toxic Substances Control**
DVBE	**Disabled Veteran Business Enterprise**
EIR	

RFI	**Request for Information**
RFB	**Request for Bid**
RFP	**Request for Proposal**
RFQ	**Request for Qualification**
SAB	**State Allocation Board**
SBCTC	**State Building and Construction Trades Council**
SBE	**State Board of Education**
SFID	
